

2013 El Paso County Comprehensive Mobility Plan



AGENDA 2013 CMP Project Map Project Listing Project Updates Projects in Design Projects under Construction Projects being Funded by CRRMA Recently Completed Projects

2013 CMP Project Map





2013 EL PASO COUNTY COMPREHENSIVE MOBILITY PLAN

PROJECTS

VRF I

- Old Hueco Tanks Road
- Eastlake Phase II
- Rojas Drive
- Greg/Edgemere Extension
- Mission Ridge Boulevard
- Vista del Sol Drive
- Darrington Road
- Pellicano Drive
- Mission Ridge Boulevard Phase II

VRF I





2013 CMP County/CRRMA Projects



PROJECTS CURRENTLY UNDERWAY

Projects in Design:

- Darrington Rd. (From Eastlake to Pellicano)
- **❖** Mission Ridge II (From Mission Ridge I to ½ mile south)
- **❖** Pellicano (From Lp375 to Darrington Rd.)

Projects under Construction:

- **❖** Vista Del Sol Dr. (From Loop 375 to Cherrington Dr.)
- **❖** Old Hueco Tanks (From North Loop to I-10)
- **❖** Rojas Dr. (From Bill Burnett Dr. to Eastlake Blvd.)
- Eastlake I (From I-10 to Darrington Rd.)

Projects being Funded by the CRRMA:

Greg/Edgemere (From Edgemere Blvd. east to Greg Rd.)

2013 CMP County/CRRMA Projects



COMPLETED PROJECTS

- Mission Ridge Blvd (from Pellicano to 1 mile south)
- ❖ El Camino Real de Tierra Adentro National Historic Trail (Along SH 20 from Chicken Rd. to NM/TX state line)
- Eastlake 2 (From Darrington Rd. to Horizon Blvd)

Darrington Road





2013 EL PASO COUNTY COMPREHENSIVE MOBILITY PLAN

PROJECTS

VRF I

- Old Hueco Tanks Road
- Eastlake Phase II
- Rojas Drive
- Greg/Edgemere Extension
- Mission Ridge Boulevard
- Vista del Sol Drive
- Darrington Road
- Pellicano Drive
- Mission Ridge Boulevard Phase II

VRF II





Darrington Road



 Widen to a 4 lane divided roadway from Eastlake to Pellicano

• PS&E Contract amount \$946,071.16

• Invoiced to Date \$914,914.08

- Working on Pellicano Intersection and finalizing drainage plans
- Construction Estimate \$9.9M
- Anticipated Letting Summer 2019



- Mission Ridge Phase II





2013 EL PASO COUNTY COMPREHENSIVE MOBILITY PLAN

PROJECTS

VRF I

- Old Hueco Tanks Road
- Eastlake Phase II
- Rojas Drive
- Greg/Edgemere Extension
- Mission Ridge Boulevard
- Vista del Sol Drive
- Darrington Road
- Pellicano Drive
- Mission Ridge Boulevard Phase II

VRF I





Mission Ridge Phase II



- 6 lane divided roadway with raised median, asphalt pavement, curb and gutter, sidewalk, landscaping, illumination and storm drainage
- 95% Design
- Construction Estimate \$5.2M
- Anticipated Letting Winter 2019

- Pellicano Drive





2013 EL PASO COUNTY COMPREHENSIVE MOBILITY PLAN

PROJECTS

VRF I

- Old Hueco Tanks Road
- Eastlake Phase II
- Rojas Drive
- Greg/Edgemere Extension
- Mission Ridge Boulevard
- Vista del Sol Drive
- Darrington Road
- Pellicano Drive
- Mission Ridge Boulevard Phase II

VRF II





- Pellicano Drive



- 6 lane divided roadway with bike lanes, hike and bike trail, illumination, and landscaping
- PS&E Contract amount \$1,965,422.17
- Invoiced to Date \$1,286,652.85
- 95% Schematic/95% Design
- Construction Estimate \$21M (VRF 1 and Federal funding)
- Anticipated Letting Summer 2019

Projects in Construction – Vista Del Sol Dr.





2013 EL PASO COUNTY COMPREHENSIVE MOBILITY PLAN

PROJECTS

VRF I

- Old Hueco Tanks Road
- Eastlake Phase II
- Rojas Drive
- Greg/Edgemere Extension
- Mission Ridge Boulevard
- Vista del Sol Drive
- Darrington Road
- Pellicano Drive
- Mission Ridge Boulevard Phase II

VRF II





Vista Del Sol Dr.



 Widen to a 4 lane divided roadway from Loop 375 to Cherrington Dr.

Bain Construction

• Contract Amount \$4,582,190.00

Adjusted Contract Amount

With Change Orders \$4,858,608.33

• Invoiced to Date \$3,085,405.66

• Complete to Date 63.50%

 Working on installation of landscape items and clean-up for final walkthrough inspection of Phase I (Paseo Grande to Cherrington)

Projects in Construction – Vista Del Sol Dr.



Installation of Landscape Items - Looking East



Projects in Construction – Vista Del Sol Dr.



Clean up – Looking East



Projects in ConstructionOld Hueco Tanks Road





2013 EL PASO COUNTY COMPREHENSIVE MOBILITY PLAN

PROJECTS

VRF I

- Old Hueco Tanks Road
- Eastlake Phase II
- Rojas Drive
- Greg/Edgemere Extension
- Mission Ridge Boulevard
- Vista del Sol Drive
- Darrington Road
- Pellicano Drive
- Mission Ridge Boulevard Phase II

VRF II





Old Hueco Tanks Road



 New 4 lane divided roadway – Signed as Nuevo Hueco Tanks Road

International Eagle Enterprises, Inc.

• Contract Amount \$7,520,127.90

Adjusted Contract Amount

With Change Orders \$7,857,588.67

Invoiced to Date \$7,509,351.33

• Complete to Date 95.57%

Working on closeout documents

Projects in ConstructionOld Hueco Tanks Road



Open to Traffic – Looking North



Projects in ConstructionOld Hueco Tanks Road



Open to Traffic – Looking South



Rojas Drive





2013 EL PASO COUNTY COMPREHENSIVE MOBILITY PLAN

PROJECTS

VRF I

- Old Hueco Tanks Road
- Eastlake Phase II
- Rojas Drive
- Greg/Edgemere Extension
- Mission Ridge Boulevard
- Vista del Sol Drive
- Darrington Road
- Pellicano Drive
- Mission Ridge Boulevard Phase II

VRF II





Rojas Drive



- Widen Rojas to a 6 lane divided roadway (El Paso City limits to Eastlake Blvd.)
- Horizone Construction, LTD

• Contract \$3,843,033.70

Adjusted Contract Amount

With Change Orders \$4,132,243.38

• Invoiced to Date \$3,832,222.65

• Complete to Date 92.74%

Opened to the public on September 11, 2018

Rojas Drive



Open to Traffic – Looking East



Rojas Drive



Open to Traffic – Looking East



- Eastlake Phase I





2013 EL PASO COUNTY COMPREHENSIVE MOBILITY PLAN

PROJECTS

VRF I

- Old Hueco Tanks Road
- Eastlake Phase II
- Rojas Drive
- Greg/Edgemere Extension
- Mission Ridge Boulevard
- Vista del Sol Drive
- Darrington Road
- Pellicano Drive
- Mission Ridge Boulevard Phase II

VRF I





Eastlake Phase I



 Widen to 6 lane divided roadway with raised median (I-10 to Darrington Rd.)

JD Abrams, LLP

• Contract \$23,653,752.53

Adjusted Contract Amount

With Change Orders \$23,654,752.53

• Invoiced to Date \$5,695,490.79

• Complete to Date 24.08%

Phase I-A Eastlake NB opened to traffic from Rojas to Peyton

 Phase I-B Eastlake NB ongoing construction from Peyton to Darrington. Working on installation of Storm Sewer, Excavation/Embankment, Flex Base, and Concrete Pavement

Projects in Construction – Eastlake Phase I



Phase IA (Rojas to Peyton) – Open to Traffic looking South



Projects in Construction – Eastlake Phase I




Phase IB (Peyton to Darrington) – Excavation/Embankment



- Eastlake Phase I



Phase IB (Peyton to Darrington) – Installing Storm Sewer

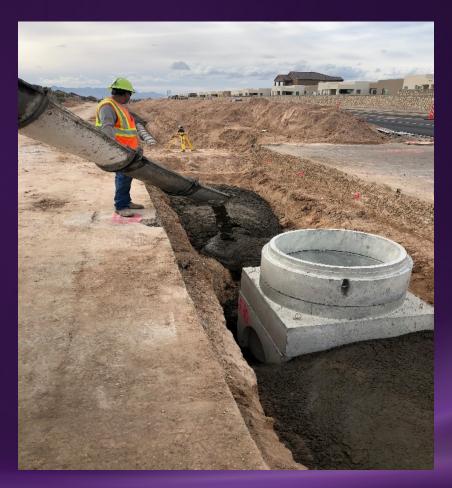

- Greg/Edgemere Extension





2013 EL PASO COUNTY COMPREHENSIVE MOBILITY PLAN

PROJECTS

VRF I

- Old Hueco Tanks Road
- Eastlake Phase II
- Rojas Drive
- Greg/Edgemere Extension
- Mission Ridge Boulevard
- Vista del Sol Drive
- Darrington Road
- Pellicano Drive
- Mission Ridge Boulevard Phase II

VRF II





- Greg/Edgemere Extension



- Greg/Edgemere Extension 4 lanes divided w/ bike lanes (Edgemere Blvd east 1.3 miles to Greg Rd.)
- CRRMA funding the construction via payment to County \$2.5M
- Work done thru a County Developer Participation Agreement
- Contractor working on final punch list items

- Greg/Edgemere Extension



Open to Traffic – Looking West (Idea School)



- Greg/Edgemere Extension




Open to Traffic – Looking East (Idea School)



Recently Completed Projects – Camino Real National Historic Trail



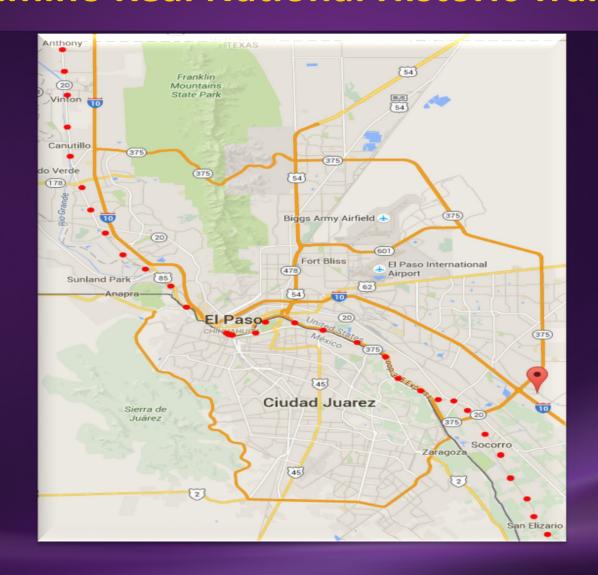

Recently Completed Projects - Camino Real National Historic Trail



- Historic signage from San Elizario to Anthony, Texas
- Lesna Construction Inc.
- Contract Amount \$157,685.00
- Adjusted Contract Amount
 With Change Orders \$157,187.88
- Invoiced to Date \$157,187.88
- Complete to date 100%
- Project is complete

Recently Completed Projects – Camino Real National Historic Trail



Installed Signs





Recently Completed Projects - Eastlake Phase 2





2013 EL PASO COUNTY COMPREHENSIVE MOBILITY PLAN

PROJECTS

VRF I

- Old Hueco Tanks Road
- Eastlake Phase II
- Rojas Drive
- Greg/Edgemere Extension
- Mission Ridge Boulevard
- Vista del Sol Drive
- Darrington Road
- Pellicano Drive
- Mission Ridge Boulevard Phase II

VRF II





Recently Completed Projects

– Eastlake Phase 2



- Widen to a 6 lane divided roadway (Darrington Rd. to Horizon Blvd.)
- Jordan Foster Construction

• Contract Amount \$13,464,149.00

Adjusted Contract Amount

With Change Orders \$13,772,538.58

• Invoiced to Date \$13,768,278.58

• Complete to Date 99.97%

 Construction activities are now complete. Plant and irrigation maintenance will continue, per contract.

Recently Completed Projects - Eastlake Phase 2



Open to Traffic – Kenazo Intersection Looking East



Questions?



