



**CAMINO REAL**  
REGIONAL MOBILITY  
AUTHORITY

## **CRRMA BOARD PRESENTATION**

# **2013 EL PASO COUNTY COMPREHENSIVE MOBILITY PLAN UPDATE**

**Edgar Fino  
June 12, 2019**

# 2013 El Paso County Comprehensive Mobility Plan



## AGENDA

- 2013 CMP Project Map
- Project Listing
- Project Updates
  - Projects in Design
  - Projects under Construction
  - Projects being Funded by CRRMA
  - Projects Constructed



# 2013 CMP Project Map



## 2013 EL PASO COUNTY COMPREHENSIVE MOBILITY PLAN

### PROJECTS

#### VRF I

-  Old Hueco Tanks Road
-  Eastlake Phase II
-  Rojas Drive
-  Greg/Edgemere Extension
-  Mission Ridge Boulevard
-  Vista del Sol Drive
-  Darrington Road
-  Pellicano Drive
-  Mission Ridge Boulevard Phase II

#### VRF II

-  Eastlake Phase I



# 2013 CMP Project List

## Projects in Design:

- ❖ Darrington Rd. (From Eastlake to Pellicano)
- ❖ Mission Ridge II (From Mission Ridge I to ½ mile south)
- ❖ Pellicano (From Lp375 to Darrington Rd.)
- ❖ O.T. Smith (From Alameda Ave. to I-10)

## Projects under Construction:

- ❖ Vista Del Sol Dr. (From Loop 375 to Cherrington Dr.)
- ❖ Rojas Dr. (From Bill Burnett Dr. to Eastlake Blvd.)
- ❖ Eastlake I (From I-10 to Darrington Rd.)

## Completed Projects:

- ❖ Greg/Edgemere (From Edgemere Blvd. east to Greg Rd.)
- ❖ Old Hueco Tanks (From North Loop to I-10)
- ❖ El Camino Real de Tierra Adentro National Historic Trail  
(Along SH 20 from Chicken Rd. to NM/TX state line)
- ❖ Eastlake 2 (From Darrington Rd. to Horizon Blvd)

# Projects in Design

## – Darrington Road



### 2013 EL PASO COUNTY COMPREHENSIVE MOBILITY PLAN

#### PROJECTS

##### VRF I

- Old Hueco Tanks Road
- Eastlake Phase II
- Rojas Drive
- Greg/Edgemere Extension
- Mission Ridge Boulevard
- Vista del Sol Drive
- Darrington Road
- Pellicano Drive
- Mission Ridge Boulevard Phase II

##### VRF II

- Eastlake Phase I



# Projects in Design

## – Darrington Road

- Widen to a 4 lane divided roadway from Eastlake to Pellicano
- PS&E Contract amount \$999,963.58
- **Invoiced to Date                      \$972,788.76**
- **Finalizing drainage plans**
- Construction Estimate – \$9.9M
- Anticipated Letting – Winter 2019



# Projects in Design

## – Mission Ridge Phase II



### 2013 EL PASO COUNTY COMPREHENSIVE MOBILITY PLAN

#### PROJECTS

##### VRF I

- Old Hueco Tanks Road
- Eastlake Phase II
- Rojas Drive
- Greg/Edgemere Extension
- Mission Ridge Boulevard
- Vista del Sol Drive
- Darrington Road
- Pellicano Drive
- Mission Ridge Boulevard Phase II

##### VRF II

- Eastlake Phase I



# Projects in Design

## – Mission Ridge Phase II

- 6 lane divided roadway with raised median, asphalt pavement, curb and gutter, sidewalk, landscaping, illumination and storm drainage
- 100% Design
- Construction Estimate – \$5.7M
- **Letting Date – June 7, 2019**
- **Award Date – June 12, 2019 (proposed)**

# Projects in Design – Pellicano Drive



## 2013 EL PASO COUNTY COMPREHENSIVE MOBILITY PLAN

### PROJECTS

#### VRF I

- Old Hueco Tanks Road
- Eastlake Phase II
- Rojas Drive
- Greg/Edgemere Extension
- Mission Ridge Boulevard
- Vista del Sol Drive
- Darrington Road
- Pellicano Drive
- Mission Ridge Boulevard Phase II

#### VRF II

- Eastlake Phase I



# Projects in Design

## – Pellicano Drive

- 6 lane divided roadway with bike lanes, hike and bike trail, illumination and landscaping
- PS&E Contract amount \$1,965,422.17
- **Invoiced to Date \$1,946,576.21**
- **100% Schematic/100% Design**
- Construction Estimate - \$28M (VRF 1 and Fed funds)
- **Anticipated Letting - Fall 2019**

# Projects in Design


## – O.T. Smith Shared Use Path



# Projects in Design

## – O.T. Smith Shared Use Path

- Construction of a 8' to 12' wide shared use path from Alameda Ave. to I-10.
- 100% Design
- Construction Estimate – \$2.6M
- Anticipated Letting – Summer 2019

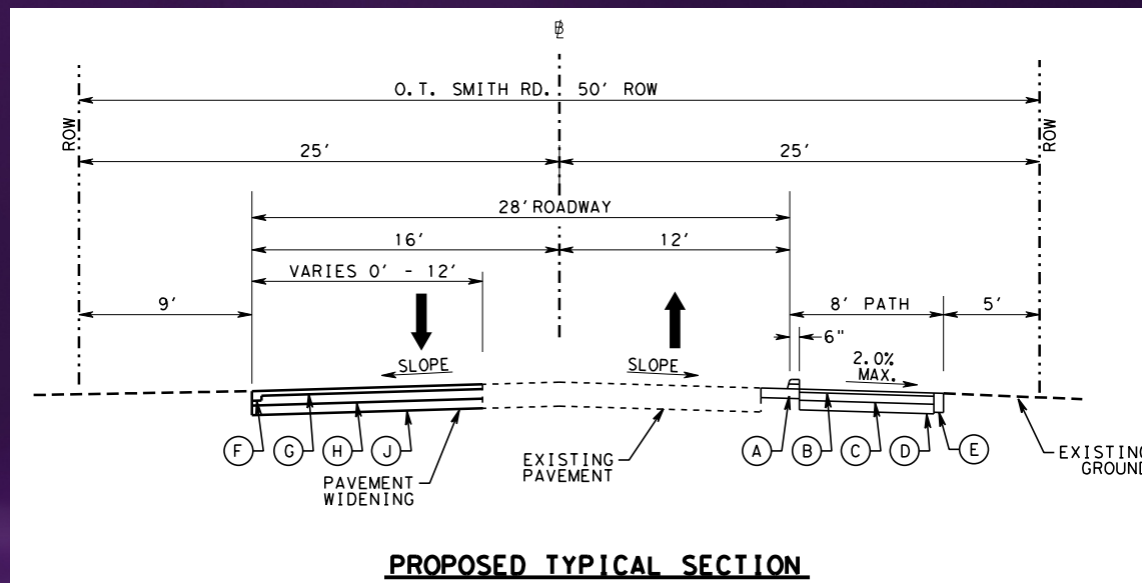

# Projects in Construction

## – Vista Del Sol Dr.



### 2013 EL PASO COUNTY COMPREHENSIVE MOBILITY PLAN

#### PROJECTS

##### VRF I

- Old Hueco Tanks Road
- Eastlake Phase II
- Rojas Drive
- Greg/Edgemere Extension
- Mission Ridge Boulevard
- Vista del Sol Drive
- Darrington Road
- Pellicano Drive
- Mission Ridge Boulevard Phase II

##### VRF II

- Eastlake Phase I



# Projects in Construction

## – Vista Del Sol Dr.

- Widen to a 4 lane divided roadway from LP375 to Cherrington Dr.
- Bain Construction
- Contract Amount \$4,582,190.00
- Contract Amount (w/COs) \$4,892,342.92
- Invoiced to Date \$3,884,370.02
- Complete to Date 79.39%
- Installation of irrigation, landscape and sidewalk within Phase II and III of the project between Paseo Grande St. and Joe Battle Ave. is in progress
- Phase I open to traffic from Paseo Grande St. to Cherrington St.

# Projects in Construction

## – Vista Del Sol Dr.

Phase I – Open to Traffic from Paseo Grande St. to Cherrington St.



# Projects in Construction

## – Vista Del Sol Dr.

### Phase 2 & 3 – Irrigation Installation



# Projects in Construction

## – Rojas Drive



### 2013 EL PASO COUNTY COMPREHENSIVE MOBILITY PLAN

#### PROJECTS

##### VRF I

- Old Hueco Tanks Road
- Eastlake Phase II
- Rojas Drive
- Greg/Edgemere Extension
- Mission Ridge Boulevard
- Vista del Sol Drive
- Darrington Road
- Pellicano Drive
- Mission Ridge Boulevard Phase II

##### VRF II

- Eastlake Phase I



# Projects in Construction

## – Rojas Drive

- Widen Rojas to a 6 lane divided roadway (El Paso City limits to Eastlake Blvd.)
- Horizone Construction, LTD
- Contract Amount \$3,843,033.70
- Contract Amount (w/COs) \$4,138,910.57
- Invoiced to Date \$3,857,258.09
- Complete to Date 93.20%
- Working on closeout documents
- Open to traffic

# Projects in Construction

## – Eastlake Phase I



### 2013 EL PASO COUNTY COMPREHENSIVE MOBILITY PLAN

#### PROJECTS

##### VRF I

- Old Hueco Tanks Road
- Eastlake Phase II
- Rojas Drive
- Greg/Edgemere Extension
- Mission Ridge Boulevard
- Vista del Sol Drive
- Darrington Road
- Pellicano Drive
- Mission Ridge Boulevard Phase II

##### VRF II

- Eastlake Phase I



# Projects in Construction

## – Eastlake Phase I

- Widen to 6 lane divided roadway with raised median (I-10 to Darrington Rd.)
- JD Abrams, LLP
- Contract Amount \$23,653,752.53
- Contract Amount \$23,686,786.42
- Invoiced to Date \$10,498,500.56
- Complete to Date 44.32%
- Phase I Eastlake NB opened to traffic in both directions from Rojas to Darrington Road
- Phase II Eastlake SB ongoing construction from Darrington Road to Rojas. Working on installation of storm sewer, embankment, flex base, asphalt, and concrete pavement

# Projects in Construction

## – Eastlake Phase I

Phase II ( Emerald Park Dr.) looking South



# Projects in Construction

## – Eastlake Phase I

Phase II (Looking North) – Laying asphalt and placing rebar



# Completed Projects

## – Greg/Edgemere Extension



### 2013 EL PASO COUNTY COMPREHENSIVE MOBILITY PLAN

#### PROJECTS

##### VRF I

- Old Hueco Tanks Road
- Eastlake Phase II
- Rojas Drive
- Greg/Edgemere Extension
- Mission Ridge Boulevard
- Vista del Sol Drive
- Darrington Road
- Pellicano Drive
- Mission Ridge Boulevard Phase II

##### VRF II

- Eastlake Phase I



# Completed Projects

## – Greg/Edgemere Extension Project



- **Greg/Edgemere Extension – 4 lanes divided w/ bike lanes (Edgemere Blvd east 1.3 miles to Greg Rd.)**
- **CRRMA funding the construction via payment to County – \$2.5M**
- **Work done thru a County Developer Participation Agreement**
- **Open to traffic**

# Completed Projects

## – Greg/Edgemere Extension Project

Open to Traffic – Looking West (Idea School)



# Completed Projects

## – Greg/Edgemere Extension Project

Open to Traffic – Looking East (Idea School)



# Completed Projects

## – Old Hueco Tanks Road



### 2013 EL PASO COUNTY COMPREHENSIVE MOBILITY PLAN

#### PROJECTS

##### VRF I

- Old Hueco Tanks Road
- Eastlake Phase II
- Rojas Drive
- Greg/Edgemere Extension
- Mission Ridge Boulevard
- Vista del Sol Drive
- Darrington Road
- Pellicano Drive
- Mission Ridge Boulevard Phase II

##### VRF II

- Eastlake Phase I



# Completed Projects

## – Old Hueco Tanks Road

- New 4 lane divided roadway – **Signed as *Nuevo Hueco Tanks Road***
- International Eagle Enterprises, Inc.
- Contract Amount **\$7,520,127.90**
- Contract Amount (w/COs) **\$7,876,574.31**
- **Invoiced to Date** **\$7,552,133.17**
- **Complete to Date** **95.88%**
- Working on closeout documents
- Open to traffic



**CAMINO REAL**  
REGIONAL MOBILITY  
AUTHORITY



# Completed Projects

## – Camino Real National Historic Trail



- Historic signage from San Elizario to Anthony, Texas
- Lesna Construction Inc.
- Contract Amount \$157,685.00
- Adjusted Contract Amount  
With Change Orders \$157,187.88
- Invoiced to Date \$157,187.88
- Complete to date 100%
- Project is complete

# Completed Projects

## – Camino Real National Historic Trail

### Installed Signs



# Completed Projects

## – Eastlake Phase 2



### 2013 EL PASO COUNTY COMPREHENSIVE MOBILITY PLAN

#### PROJECTS

##### VRF I

-  Old Hueco Tanks Road
-  Eastlake Phase II
-  Rojas Drive
-  Greg/Edgemere Extension
-  Mission Ridge Boulevard
-  Vista del Sol Drive
-  Darrington Road
-  Pellicano Drive
-  Mission Ridge Boulevard Phase II

##### VRF II

-  Eastlake Phase I



# Completed Projects

## – Eastlake Phase 2

- Widen to a 6 lane divided roadway (Darrington Rd. to Horizon Blvd.)
- Jordan Foster Construction
- Contract Amount **\$13,464,149.00**
- Adjusted Contract Amount  
With Change Orders **\$13,772,538.58**
- Invoiced to Date **\$13,772,538.58**
- Complete to Date **100%**
- Plant and irrigation maintenance completed

# Questions?



Camino Real Regional Mobility Authority

801 Texas Avenue

El Paso, Texas 79901

(915) 212-1072

[info@crrma.org](mailto:info@crrma.org)

[www.crrma.org](http://www.crrma.org)
