



CAMINO REAL
REGIONAL MOBILITY
AUTHORITY

CRRMA BOARD PRESENTATION

2013 EL PASO COUNTY COMPREHENSIVE MOBILITY PLAN UPDATE

Raymond Telles
June 9, 2021

2013 El Paso County Comprehensive Mobility Plan



AGENDA

- 2013 CMP Project Map
- Project Listing
- Project Updates
 - Projects in Design
 - Projects under Construction
 - Projects Constructed

2013 CMP Project Map



2013 EL PASO COUNTY COMPREHENSIVE MOBILITY PLAN

PROJECTS

VRF I

-  Old Hueco Tanks Road
-  Eastlake Phase II
-  Rojas Drive
-  Greg/Edgemere Extension
-  Mission Ridge Boulevard
-  Vista del Sol Drive
-  Darrington Road
-  Pellicano Drive
-  Mission Ridge Boulevard Phase II

VRF II

-  Eastlake Phase I



2013 CMP Project List

Projects in Design:

- ❖ Darrington Rd. (From Eastlake to Pellicano)

Projects under Construction:

- ❖ Pellicano (From LP-375 to Darrington Rd.)
- ❖ Mission Ridge II (From Mission Ridge I to ½ mile south)
- ❖ Eastlake I (From I-10 to Darrington Rd.)
- ❖ Vista Del Sol Dr. (From Loop 375 to Cherrington Dr.)

Completed Projects:

- ❖ Greg/Edgemere (From Edgemere Blvd. east to Greg Rd.)
- ❖ Old Hueco Tanks (From North Loop to I-10)
- ❖ El Camino Real de Tierra Adentro National Historic Trail
(Along SH 20 from Chicken Rd. to NM/TX state line)
- ❖ Eastlake 2 (From Darrington Rd. to Horizon Blvd)
- ❖ Rojas Dr. (From Bill Burnett Dr. to Eastlake Blvd.)

Projects in Design – Darrington Road



2013 EL PASO COUNTY COMPREHENSIVE MOBILITY PLAN

PROJECTS

VRF I

- Old Hueco Tanks Road
- Eastlake Phase II
- Rojas Drive
- Greg/Edgemere Extension
- Mission Ridge Boulevard
- Vista del Sol Drive
- Darrington Road
- Pellicano Drive
- Mission Ridge Boulevard Phase II

VRF II

- Eastlake Phase I



Projects in Design

– Darrington Road

- Widen to a 4 lane divided roadway from Eastlake to Pellicano
- PS&E Contract amount **\$1,063,474.28**
- Invoiced to Date **\$1,046,473.09**
- **Preliminary concrete design**
- Construction Estimate - \$9.9M
- Anticipated Letting – **Fall 2021**



Projects in Construction

– Pellicano Drive



2013 EL PASO COUNTY COMPREHENSIVE MOBILITY PLAN

PROJECTS

VRF I

- Old Hueco Tanks Road
- Eastlake Phase II
- Rojas Drive
- Greg/Edgemere Extension
- Mission Ridge Boulevard
- Vista del Sol Drive
- Darrington Road
- Pellicano Drive
- Mission Ridge Boulevard Phase II

VRF II

- Eastlake Phase I



Projects in Construction

– Pellicano Drive

- 6 lane divided roadway with bike lanes, hike and bike trail, illumination and landscaping
- JAR Concrete
- **Contract Amount** **\$21,655,645.80**
- **Contract Amount (w/COs)** **\$21,539,091.39**
- **Invoiced to Date** **\$ 7,044,357.74**
- **Complete to Date** **32.70%**
- Installation of flexible base, HMAC, concrete pavement, excavation of pond A & B and installation of water line.

Projects in Construction – Pellicano Drive

Looking east – Mission Ridge to Aircoupe



Projects in Construction – Pellicano Drive

Looking south – Finalizing Mission Ridge intersection



Projects in Construction

– Mission Ridge Phase II



2013 EL PASO COUNTY COMPREHENSIVE MOBILITY PLAN

PROJECTS

VRF I

-  Old Hueco Tanks Road
-  Eastlake Phase II
-  Rojas Drive
-  Greg/Edgemere Extension
-  Mission Ridge Boulevard
-  Vista del Sol Drive
-  Darrington Road
-  Pellicano Drive
-  Mission Ridge Boulevard Phase II

VRF II

-  Eastlake Phase I



Projects in Construction

– Mission Ridge Phase II

- 6 lane divided roadway with raised median, asphalt pavement, curb and gutter, sidewalk, landscaping, illumination and storm drainage
- JAR Concrete
- **Contract Amount** **\$5,162,216.00**
- **Contract Amount (w/COs)** **\$5,778,507.87**
- **Invoiced to Date** **\$5,246,806.73**
- **Complete to Date** **90.80%**
- Placing landscaping
- Constructing rock wall
- Completed sanitary sewer line

Projects in Construction

– Mission Ridge Blvd. Phase II

Looking North heading to Paseo del Este Blvd



Projects in Construction

– Mission Ridge Blvd. Phase II

Looking north on an added relief Route



Projects in Construction

– Mission Ridge Blvd. Phase II

(Pellicano Dr.) looking down at testing of a manhole for a 16" sanitary sewer line that is completed



Projects in Construction

– Eastlake Phase I



2013 EL PASO COUNTY COMPREHENSIVE MOBILITY PLAN

PROJECTS

VRF I

- Old Hueco Tanks Road
- Eastlake Phase II
- Rojas Drive
- Greg/Edgemere Extension
- Mission Ridge Boulevard
- Vista del Sol Drive
- Darrington Road
- Pellicano Drive
- Mission Ridge Boulevard Phase II

VRF II

- Eastlake Phase I



Projects in Construction

– Eastlake Phase I

- Widen to 6 lane divided roadway with raised median (I-10 to Darrington Rd.)
- JD Abrams, LLP
- **Contract Amount** **\$23,653,752.53**
- **Contract Amount (w/COs)** **\$25,814,908.90**
- **Invoiced to Date** **\$25,508,027.84**
- **Complete to Date** **98.81%**
- Eastlake Boulevard project is adding work and contractor is working on punch list items.

Projects in Construction

– Eastlake Phase I

Stem wall work- Looking north from Rojas Dr.



Projects in Construction

– Eastlake Phase I

Cleanup Phase - Looking north from Emerald Park Dr.



Projects in Construction

– Vista Del Sol Dr.



2013 EL PASO COUNTY COMPREHENSIVE MOBILITY PLAN

PROJECTS

VRF I

- Old Hueco Tanks Road
- Eastlake Phase II
- Rojas Drive
- Greg/Edgemere Extension
- Mission Ridge Boulevard
- Vista del Sol Drive
- Darrington Road
- Pellicano Drive
- Mission Ridge Boulevard Phase II

VRF II

- Eastlake Phase I



Projects in Construction

– Vista Del Sol Dr.

- Widen to a 4 lane divided roadway from LP375 to Cherrington Dr.
- Bain Construction
- Contract Amount \$4,582,190.00
- Contract Amount (w/COs) \$4,989,486.70
- Invoiced to Date \$4,989,486.70
- Complete to Date 100%
- Open to traffic
- Working on warranty items

Completed Projects

– Greg/Edgemere Extension



2013 EL PASO COUNTY COMPREHENSIVE MOBILITY PLAN

PROJECTS

VRF I

- Old Hueco Tanks Road
- Eastlake Phase II
- Rojas Drive
- Greg/Edgemere Extension
- Mission Ridge Boulevard
- Vista del Sol Drive
- Darrington Road
- Pellicano Drive
- Mission Ridge Boulevard Phase II

VRF II

- Eastlake Phase I



Completed Projects

– Greg/Edgemere Extension Project



- Greg/Edgemere Extension – 4 lanes divided w/ bike lanes (Edgemere Blvd east 1.3 miles to Greg Rd.)
- CRRMA funding the construction via payment to County – \$ 2,475,819.14
- Work done thru a County Developer Participation Agreement
- Open to traffic
- Project is complete

Completed Projects

– Old Hueco Tanks Road



2013 EL PASO COUNTY COMPREHENSIVE MOBILITY PLAN

PROJECTS

VRF I

- Old Hueco Tanks Road
- Eastlake Phase II
- Rojas Drive
- Greg/Edgemere Extension
- Mission Ridge Boulevard
- Vista del Sol Drive
- Darrington Road
- Pellicano Drive
- Mission Ridge Boulevard Phase II

VRF II

- Eastlake Phase I




Completed Projects

– Old Hueco Tanks Road

- New 4 lane divided roadway – **Signed as *Nuevo Hueco Tanks Road***
- International Eagle Enterprises, Inc.
- Contract Amount \$7,520,127.90
- Contract Amount (w/COs) \$7,601,890.60
- Invoiced to Date \$7,601,890.60
- Complete to Date 100.00%
- Open to traffic
- **Working on closeout documents**

Completed Projects

– Camino Real National Historic Trail

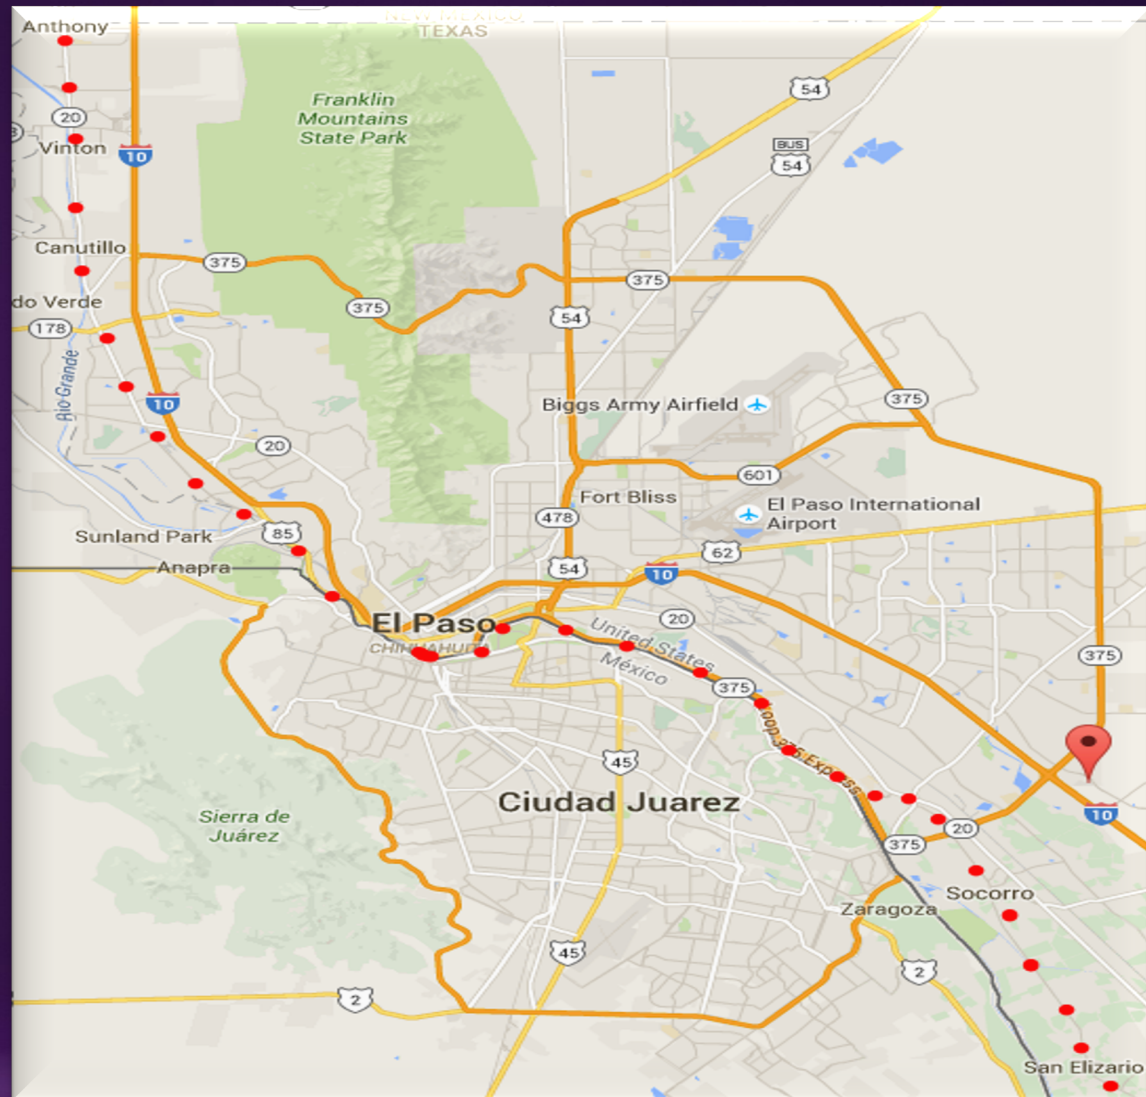

Completed Projects

– Camino Real National Historic Trail



- Historic signage from San Elizario to Anthony, Texas
- Lesna Construction Inc.
- Contract Amount \$157,685.00
- Adjusted Contract Amount
With Change Orders \$157,187.88
- Invoiced to Date \$157,187.88
- Complete to date 100%
- Project is complete

Completed Projects

– Eastlake Phase 2



2013 EL PASO COUNTY COMPREHENSIVE MOBILITY PLAN

PROJECTS

VRF I

- Old Hueco Tanks Road
- Eastlake Phase II
- Rojas Drive
- Greg/Edgemere Extension
- Mission Ridge Boulevard
- Vista del Sol Drive
- Darrington Road
- Pellicano Drive
- Mission Ridge Boulevard Phase II

VRF II

- Eastlake Phase I



Completed Projects

– Eastlake Phase 2



- Widen to a 6 lane divided roadway (Darrington Rd. to Horizon Blvd.)
- Jordan Foster Construction
- Contract Amount **\$13,464,149.00**
- Adjusted Contract Amount
With Change Orders **\$13,772,538.58**
- Invoiced to Date **\$13,772,538.58**
- Complete to Date **100%**
- Project is complete

Completed Projects

– Rojas Drive



2013 EL PASO COUNTY COMPREHENSIVE MOBILITY PLAN

PROJECTS

VRF I

- Old Hueco Tanks Road
- Eastlake Phase II
- Rojas Drive
- Greg/Edgemere Extension
- Mission Ridge Boulevard
- Vista del Sol Drive
- Darrington Road
- Pellicano Drive
- Mission Ridge Boulevard Phase II

VRF II

- Eastlake Phase I



Completed Projects

– Rojas Drive

- Widen Rojas to a 6 lane divided roadway (El Paso City limits to Eastlake Blvd.)
- Horizone Construction, LTD
- Contract Amount \$3,843,033.70
- Contract Amount (w/COs) \$3,905,601.55
- Invoiced to Date \$3,905,601.55
- Complete to Date 100%
- **Project is complete**

Questions?



Camino Real Regional Mobility Authority

801 Texas Avenue

El Paso, Texas 79901

(915) 212-1072

info@crrma.org

www.crrma.org
