

# 2013 El Paso County Comprehensive Mobility Plan



# **AGENDA 2013 CMP Project Map Project Listing Project Updates Projects in Design Projects under Construction Projects Constructed**

## 2013 CMP Project Map





## 2013 EL PASO COUNTY COMPREHENSIVE MOBILITY PLAN

### **PROJECTS**

#### VRF I

- Old Hueco Tanks Road
- Eastlake Phase II
- Rojas Drive
- Greg/Edgemere Extension
- Mission Ridge Boulevard
- Vista del Sol Drive
- Darrington Road
- Pellicano Drive
- Mission Ridge Boulevard Phase II

#### VRF II





## **2013 CMP Project List**



### **Projects in Design:**

**❖** Darrington Rd. (From Eastlake to Pellicano)

### **Projects under Construction:**

- **❖** Pellicano (From LP-375 to Darrington Rd.)
- **❖** Mission Ridge II (From Mission Ridge I to ½ mile south)
- **Eastlake I (From I-10 to Darrington Rd.)**

### **Completed Projects:**

- Greg/Edgemere (From Edgemere Blvd. east to Greg Rd.)
- Old Hueco Tanks (From North Loop to I-10)
- El Camino Real de Tierra Adentro National Historic Trail (Along SH 20 from Chicken Rd. to NM/TX state line)
- **Solution** Eastlake 2 (From Darrington Rd. to Horizon Blvd)
- Rojas Dr. (From Bill Burnett Dr. to Eastlake Blvd.)
- ❖ Vista Del Sol Dr. (From Loop 375 to Cherrington Dr.)

# Projects in Design – Darrington Road





## 2013 EL PASO COUNTY COMPREHENSIVE MOBILITY PLAN

### **PROJECTS**

#### VRF I

- Old Hueco Tanks Road
- Eastlake Phase II
- Rojas Drive
- Greg/Edgemere Extension
- Mission Ridge Boulevard
- Vista del Sol Drive
- Darrington Road
- Pellicano Drive
- Mission Ridge Boulevard Phase II

#### VRF II





## **Projects in Design**

# Darrington Road



- Widen to a 4 lane divided roadway from Eastlake to Pellicano
- PS&E Contract amount \$1,063,474.28
- Invoiced to Date \$1,046,473.09
- Preliminary concrete design
- Construction Estimate \$9.9M
- Anticipated Letting Summer 2022







## 2013 EL PASO COUNTY COMPREHENSIVE MOBILITY PLAN

### **PROJECTS**

#### VRF I

- Old Hueco Tanks Road
- Eastlake Phase II
- Rojas Drive
- Greg/Edgemere Extension
- Mission Ridge Boulevard
- Vista del Sol Drive
- Darrington Road
- Pellicano Drive
- Mission Ridge Boulevard Phase II

### VRF II





# **Projects in Construction**

## Pellicano Drive



- 6 lane divided roadway with bike lanes, hike and bike trail, illumination and landscaping
- JAR Concrete

• Contract Amount \$21,655,645.80

Contract Amount (w/COs) \$21,615,273.83

Invoiced to Date
 \$ 8,778,589.32

• Complete to Date 40.61%

 Installation of flexible base, HMAC, concrete pavement, excavation of pond A & B and installation/testing of water line.



Looking east – Installation of concrete pavement (gas station)





Looking west – HMAC completed from Aircoupe to Sunfire





Looking east – Installation of flexible base (Aircoupe to Darrington)





Pond B – Excavation complete



# Projects in Construction – Mission Ridge Phase II





## 2013 EL PASO COUNTY COMPREHENSIVE MOBILITY PLAN

### **PROJECTS**

### VRF I

- Old Hueco Tanks Road
- Eastlake Phase II
- Rojas Drive
- Greg/Edgemere Extension
- Mission Ridge Boulevard
- Vista del Sol Drive
- Darrington Road
- Pellicano Drive
- Mission Ridge Boulevard Phase II

### VRF II





# **Projects in Construction**

# - Mission Ridge Phase II



- 6 lane divided roadway with raised median, asphalt pavement, curb and gutter, sidewalk, landscaping, illumination and storm drainage
- JAR Concrete

• Contract Amount \$5,162,216.00

• Contract Amount (w/COs) \$5,778,507.87

• Invoiced to Date \$5,318,498.32

• Complete to Date 92. 04%

- Constructing rock wall
- Completed sanitary sewer line

# Projects in Construction – Mission Ridge Blvd. Phase II



Looking North heading to Paseo del Este Blvd



# **Projects in Construction**

# - Mission Ridge Blvd. Phase II




Looking north on Mission Ridge Blvd. working on sidewalk



# Projects in Construction – Mission Ridge Blvd. Phase II



Mission Ridge Blvd. water main line leak repair completed

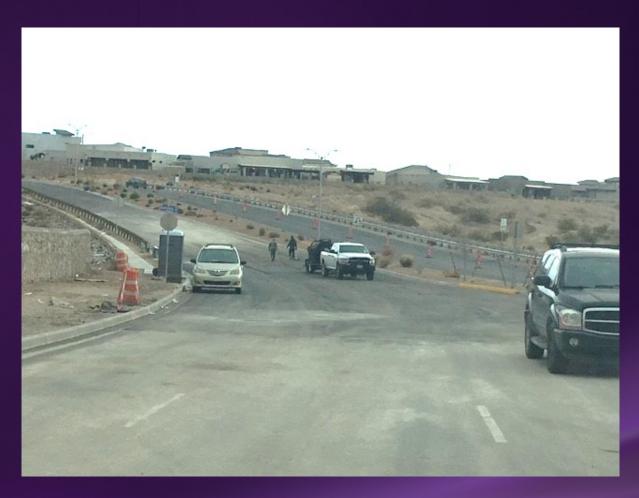

# Projects in Construction – Eastlake Phase I





## 2013 EL PASO COUNTY COMPREHENSIVE MOBILITY PLAN

### **PROJECTS**

#### VRF I

- Old Hueco Tanks Road
- Eastlake Phase II
- Rojas Drive
- Greg/Edgemere Extension
- Mission Ridge Boulevard
- Vista del Sol Drive
- Darrington Road
- Pellicano Drive
- Mission Ridge Boulevard Phase II

#### VRF II





# **Projects in Construction**



- Widen to 6 lane divided roadway with raised median (I-10 to Darrington Rd.)
- JD Abrams, LLP
- Contract Amount \$23,653,752.53
- Contract Amount (w/COs) \$ 25,786,632.50
- Invoiced to Date \$25,786,632.50
- Complete to Date 100.00%
- Roadway open to traffic
- Eastlake Boulevard project has been completed.

# Projects in Construction – Eastlake Phase I



Stem wall work- Looking north from Rojas Dr.



# Projects in Construction - Eastlake Phase I



Cleanup Phase - Looking north from Emerald Park Dr.



# Completed ProjectsVista Del Sol Dr.





## 2013 EL PASO COUNTY COMPREHENSIVE MOBILITY PLAN

### **PROJECTS**

#### VRF I

- Old Hueco Tanks Road
- Eastlake Phase II
- Rojas Drive
- Greg/Edgemere Extension
- Mission Ridge Boulevard
- Vista del Sol Drive
- Darrington Road
- Pellicano Drive
- Mission Ridge Boulevard Phase II

#### VRF II





# Completed ProjectsVista Del Sol Dr.



- Widen to a 4 lane divided roadway from LP375 to Cherrington Dr.
- Bain Construction
- Contract Amount \$4,582,190.00
- Contract Amount (w/COs) \$4,989,486.70
- Invoiced to Date \$4,989,486.70
- Complete to Date 100%
- Open to traffic
- Project is complete

# Greg/Edgemere Extension





## 2013 EL PASO COUNTY COMPREHENSIVE MOBILITY PLAN

### **PROJECTS**

#### VRF I

- Old Hueco Tanks Road
- Eastlake Phase II
- Rojas Drive
- Greg/Edgemere Extension
- Mission Ridge Boulevard
- Vista del Sol Drive
- Darrington Road
- Pellicano Drive
- Mission Ridge Boulevard Phase II

#### VRF II





## - Greg/Edgemere Extension Project



- Greg/Edgemere Extension 4 lanes divided w/ bike lanes (Edgemere Blvd east 1.3 miles to Greg Rd.)
- CRRMA funding the construction via payment to County \$ 2,475,819.14
- Work done thru a County Developer Participation Agreement
- Open to traffic
- Project is complete

# Completed Projects - Old Hueco Tanks Road





## 2013 EL PASO COUNTY COMPREHENSIVE MOBILITY PLAN

### **PROJECTS**

#### VRF I

- Old Hueco Tanks Road
- Eastlake Phase II
- Rojas Drive
- Greg/Edgemere Extension
- Mission Ridge Boulevard
- Vista del Sol Drive
- Darrington Road
- Pellicano Drive
- Mission Ridge Boulevard Phase II

### VRF II





## - Old Hueco Tanks Road



- New 4 lane divided roadway Signed as Nuevo Hueco Tanks Road
- International Eagle Enterprises, Inc.

• Contract Amount \$7,520,127.90

Contract Amount (w/COs) \$7,601,890.60


• Invoiced to Date \$7,601,890.60

Complete to Date 100.00%

- Open to traffic
- Project is completed

## - Camino Real National Historic Trail



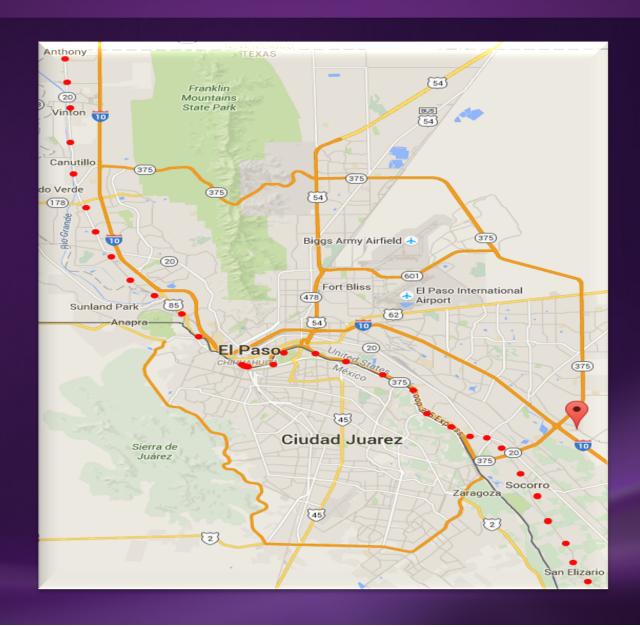

## Camino Real National Historic Trail



- Historic signage from San Elizario to Anthony, Texas
- Lesna Construction Inc.
- Contract Amount \$157,685.00
- Adjusted Contract Amount

With Change Orders \$157,187.88

- Invoiced to Date \$157,187.88
- Complete to date 100%
- Project is complete

# Completed Projects - Eastlake Phase 2





## 2013 EL PASO COUNTY COMPREHENSIVE MOBILITY PLAN

### **PROJECTS**

#### VRF I

- Old Hueco Tanks Road
- Eastlake Phase II
- Rojas Drive
- Greg/Edgemere Extension
- Mission Ridge Boulevard
- Vista del Sol Drive
- Darrington Road
- Pellicano Drive
- Mission Ridge Boulevard Phase II

#### VRF II





## Eastlake Phase 2



 Widen to a 6 lane divided roadway (Darrington Rd. to Horizon Blvd.)

Jordan Foster Construction

• Contract Amount \$13,464,149.00

Adjusted Contract Amount

With Change Orders \$13,772,538.58

• Invoiced to Date \$13,772,538.58

• Complete to Date 100%

Project is complete

# Completed Projects - Rojas Drive





## 2013 EL PASO COUNTY COMPREHENSIVE MOBILITY PLAN

#### **PROJECTS**

#### VRF I

- Old Hueco Tanks Road
- Eastlake Phase II
- Rojas Drive
- Greg/Edgemere Extension
- Mission Ridge Boulevard
- Vista del Sol Drive
- Darrington Road
- Pellicano Drive
- Mission Ridge Boulevard Phase II

#### VRF II





## Rojas Drive



- Widen Rojas to a 6 lane divided roadway (El Paso City limits to Eastlake Blvd.)
- Horizone Construction, LTD
- Contract Amount \$3,843,033.70
- Contract Amount (w/COs) \$3,905,601.55
- Invoiced to Date \$3,905,601.55
- Complete to Date 100%
- Project is complete

## **Questions?**



Camino Real Regional Mobility Authority 801 Texas Avenue El Paso, Texas 79901 (915) 212-1072 info@crrma.org www.crrma.org
