

2013 El Paso County Comprehensive Mobility Plan



AGENDA 2013 CMP Project Map Project Listing Project Updates Projects in Design Projects under Construction Projects Constructed

2013 CMP Project Map





2013 EL PASO COUNTY COMPREHENSIVE MOBILITY PLAN

PROJECTS

VRF I

- Old Hueco Tanks Road
- Eastlake Phase II
- Rojas Drive
- Greg/Edgemere Extension
- Mission Ridge Boulevard
- Vista del Sol Drive
- Darrington Road
- Pellicano Drive
- Mission Ridge Boulevard Phase II

VRF II





2013 CMP Project List



Projects in Design:

❖ Darrington Rd. (From Eastlake to Pellicano)

Projects under Construction:

- ❖ Pellicano (From LP-375 to Darrington Rd.)
- **❖** Mission Ridge II (From Mission Ridge I to ½ mile south)

Completed Projects:

- Greg/Edgemere (From Edgemere Blvd. east to Greg Rd.)
- Old Hueco Tanks (From North Loop to I-10)
- El Camino Real de Tierra Adentro National Historic Trail (Along SH 20 from Chicken Rd. to NM/TX state line)
- **Eastlake 2 (From Darrington Rd. to Horizon Blvd)**
- * Rojas Dr. (From Bill Burnett Dr. to Eastlake Blvd.)
- ❖ Vista Del Sol Dr. (From Loop 375 to Cherrington Dr.)
- **Eastlake I (From I-10 to Darrington Rd.)**

Projects in Design – Darrington Road





2013 EL PASO COUNTY COMPREHENSIVE MOBILITY PLAN

PROJECTS

VRF I

- Old Hueco Tanks Road
- Eastlake Phase II
- Rojas Drive
- Greg/Edgemere Extension
- Mission Ridge Boulevard
- Vista del Sol Drive
- Darrington Road
- Pellicano Drive
- Mission Ridge Boulevard Phase II

VRF II





Projects in Design

Darrington Road



- Widen to a 6-lane divided roadway from Eastlake to Pellicano
- PS&E Contract amount \$1,063,474.28
- Invoiced to Date \$1,046,473.09
- Preliminary concrete design
- Construction Estimate \$21M
- Anticipated Letting Summer 2026



Projects in Construction - Pellicano Drive





2013 EL PASO COUNTY COMPREHENSIVE MOBILITY PLAN

PROJECTS

VRF I

- Old Hueco Tanks Road
- Eastlake Phase II
- Rojas Drive
- Greg/Edgemere Extension
- Mission Ridge Boulevard
- Vista del Sol Drive
- Darrington Road
- Pellicano Drive
- Mission Ridge Boulevard Phase II

VRF II





Projects in Construction

- Pellicano Drive



 6 lane divided roadway with bike lanes, hike and bike trail, illumination and landscaping

JAR Concrete

Contract Amount \$21,655,645.80

Contract Amount (w/COs) \$22,183,591.43

• Invoiced to Date \$10,515,647.20

• Complete to Date 47.40%

Maintain traffic control signs & barricades due to default process

Ongoing developer coordination

Projects in Construction - Pellicano Drive



Existing Inventory on corner of Pelicano Drive & Peyton Road



Projects in Construction – Pellicano Drive



Traffic control continuing to be maintained



Projects in Construction – Mission Ridge Phase II





2013 EL PASO COUNTY COMPREHENSIVE MOBILITY PLAN

PROJECTS

VRF I

- Old Hueco Tanks Road
- Eastlake Phase II
- Rojas Drive
- Greg/Edgemere Extension
- Mission Ridge Boulevard
- Vista del Sol Drive
- Darrington Road
- Pellicano Drive
- Mission Ridge Boulevard Phase II

VRF II





Projects in Construction

- Mission Ridge Phase II



 6 lane divided roadway with raised median, asphalt pavement, curb and gutter, sidewalk, landscaping, illumination and storm drainage

JAR Concrete

• Contract Amount \$5,162,216.00

• Contract Amount (w/COs) \$5,831,054.67

• Invoiced to Date \$5,551,541.48

• Complete to Date 95. 21%

Constructing rock wall

Damaged Pipe Repair (Stopped)

Completed sanitary sewer line

Completed Projects Eastlake Phase I





2013 EL PASO COUNTY COMPREHENSIVE MOBILITY PLAN

PROJECTS

VRF I

- Old Hueco Tanks Road
- Eastlake Phase II
- Rojas Drive
- Greg/Edgemere Extension
- Mission Ridge Boulevard
- Vista del Sol Drive
- Darrington Road
- Pellicano Drive
- Mission Ridge Boulevard Phase II

VRF II





Projects in Construction – Mission Ridge Blvd. Phase II



Roadway repaired completed after waterline Leak



Eastlake Phase I



- Widen to 6 lane divided roadway with raised median (I-10 to Darrington Rd.)
- JD Abrams, LLP
- Contract Amount
- Contract Amount (w/COs)
- Invoiced to Date
- Complete to Date
- Roadway open to traffic
- Project is completed.

\$23,653,752.53

\$ 25,786,632.50

\$25,786,632.50

100.00%

Completed ProjectsVista Del Sol Dr.





2013 EL PASO COUNTY COMPREHENSIVE MOBILITY PLAN


PROJECTS

VRF I

- Old Hueco Tanks Road
- Eastlake Phase II
- Rojas Drive
- Greg/Edgemere Extension
- Mission Ridge Boulevard
- Vista del Sol Drive
- Darrington Road
- Pellicano Drive
- Mission Ridge Boulevard Phase II

VRF II



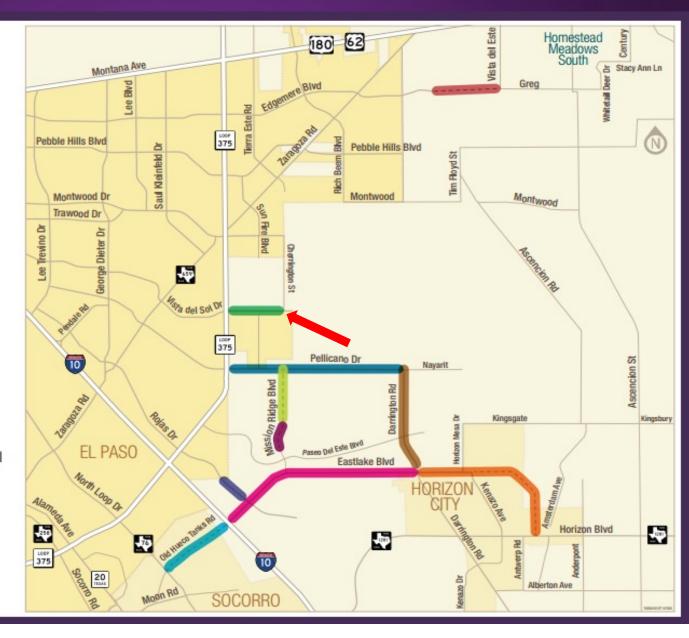

Completed ProjectsVista Del Sol Dr.



- Widen to a 4 lane divided roadway from LP375 to Cherrington Dr.
- Bain Construction
- Contract Amount
- Contract Amount (w/COs)
- Invoiced to Date
- Complete to Date
- Open to traffic
- Project is complete

\$4,582,190.00

\$4,989,486.70

\$4,989,486.70

100%

Greg/Edgemere Extension





2013 EL PASO COUNTY COMPREHENSIVE MOBILITY PLAN

PROJECTS

VRF I

- Old Hueco Tanks Road
- Eastlake Phase II
- Rojas Drive
- Greg/Edgemere Extension
- Mission Ridge Boulevard
- Vista del Sol Drive
- Darrington Road
- Pellicano Drive
- Mission Ridge Boulevard Phase II

VRF II





Greg/Edgemere Extension Project



- Greg/Edgemere Extension 4 lanes divided w/ bike lanes (Edgemere Blvd east 1.3 miles to Greg Rd.)
- CRRMA funding the construction via payment to County \$ 2,475,819.14
- Work done thru a County Developer Participation Agreement
- Open to traffic
- Project is complete

Completed Projects - Old Hueco Tanks Road





2013 EL PASO COUNTY COMPREHENSIVE MOBILITY PLAN

PROJECTS

VRF I

- Old Hueco Tanks Road
- Eastlake Phase II
- Rojas Drive
- Greg/Edgemere Extension
- Mission Ridge Boulevard
- Vista del Sol Drive
- Darrington Road
- Pellicano Drive
- Mission Ridge Boulevard Phase II

VRF II





- Old Hueco Tanks Road



- New 4 lane divided roadway Signed as Nuevo Hueco Tanks Road
- International Eagle Enterprises, Inc.

• Contract Amount \$7,520,127.90

• Contract Amount (w/COs) \$7,601,890.60

• Invoiced to Date \$7,601,890.60


Complete to Date 100.00%

Open to traffic

Project is completed

- Camino Real National Historic Trail



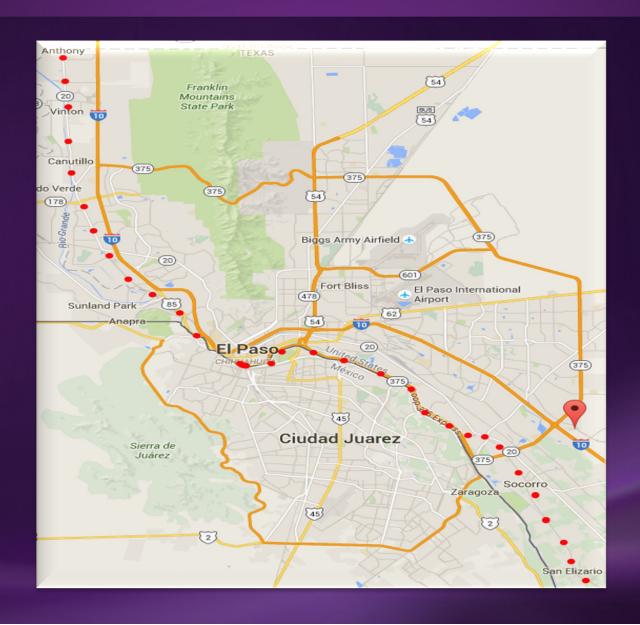

Camino Real National Historic Trail



- Historic signage from San Elizario to Anthony, Texas
- Lesna Construction Inc.
- Contract Amount \$157,685.00
- Adjusted Contract Amount
 - With Change Orders \$157,187.88
- Invoiced to Date \$157,187.88
- Complete to date 100%
- Project is complete

Completed Projects - Eastlake Phase 2





2013 EL PASO COUNTY COMPREHENSIVE MOBILITY PLAN

PROJECTS

VRF I

- Old Hueco Tanks Road
- Eastlake Phase II
- Rojas Drive
- Greg/Edgemere Extension
- Mission Ridge Boulevard
- Vista del Sol Drive
- Darrington Road
- Pellicano Drive
- Mission Ridge Boulevard Phase II

VRF II





Eastlake Phase 2



 Widen to a 6 lane divided roadway (Darrington Rd. to Horizon Blvd.)

Jordan Foster Construction

• Contract Amount \$13,464,149.00

Adjusted Contract Amount

With Change Orders \$13,772,538.58

• Invoiced to Date \$13,772,538.58

• Complete to Date 100%

Project is complete

Completed Projects - Rojas Drive





2013 EL PASO COUNTY COMPREHENSIVE MOBILITY PLAN

PROJECTS

VRF I

- Old Hueco Tanks Road
- Eastlake Phase II
- Rojas Drive
- Greg/Edgemere Extension
- Mission Ridge Boulevard
- Vista del Sol Drive
- Darrington Road
- Pellicano Drive
- Mission Ridge Boulevard Phase II

VRF II





Rojas Drive



- Widen Rojas to a 6 lane divided roadway (El Paso City limits to Eastlake Blvd.)
- Horizone Construction, LTD
- Contract Amount \$3,843,033.70
- Contract Amount (w/COs) \$3,905,601.55
- Invoiced to Date \$3,905,601.55
- Complete to Date 100%
- Project is complete

Questions?



Camino Real Regional Mobility Authority 801 Texas Avenue El Paso, Texas 79901 (915) 212-1072 info@crrma.org www.crrma.org
