



CAMINO REAL
REGIONAL MOBILITY
AUTHORITY

CRRMA BOARD PRESENTATION

2013 EL PASO COUNTY COMPREHENSIVE MOBILITY PLAN UPDATE

David Head
February 14, 2018

2013 El Paso County Comprehensive Mobility Plan



AGENDA

- 2013 CMP Project Map
- Project Listing
- Project Updates
 - Projects in Design
 - Projects under Construction
 - Projects being Funded by CRRMA



2013 CMP Project Map



2013 EL PASO COUNTY COMPREHENSIVE MOBILITY PLAN

PROJECTS

VRF I

-  Old Hueco Tanks Road
-  Eastlake Phase II
-  Rojas Drive
-  Greg/Edgemere Extension
-  Mission Ridge Boulevard
-  Vista del Sol Drive
-  Darrington Road
-  Pellicano Drive
-  Mission Ridge Boulevard Phase II

VRF II

-  Eastlake Phase I



2013 CMP County/CRRMA Projects



Projects in Design:

- ❖ Darrington Rd. (From Eastlake to Pellicano)
- ❖ Mission Ridge II (From Mission Ridge I to ½ mile south)
- ❖ Pellicano (From Lp375 to Darrington Rd.)

Projects under Construction:

- ❖ El Camino Real de Tierra Adentro National Historic Trail
(Along SH 20 from Chicken Rd. to NM/TX state line)
- ❖ Vista Del Sol Dr. (From Loop 375 to Cherrington Dr.)
- ❖ Old Hueco Tanks (From North Loop to I-10)
- ❖ Eastlake 2 (From Darrington Rd. to Horizon Blvd)
- ❖ Rojas Dr. (From Bill Burnett Dr. to Eastlake Blvd.)
- ❖ **Eastlake I (From I-10 to Darrington Rd.)**

Projects being Funded by the CRRMA:

- ❖ Greg/Edgemere (From Edgemere Blvd. east to Greg Rd.)

Projects in Design – Darrington Road



2013 EL PASO COUNTY COMPREHENSIVE MOBILITY PLAN

PROJECTS

VRF I

- Old Hueco Tanks Road
- Eastlake Phase II
- Rojas Drive
- Greg/Edgemere Extension
- Mission Ridge Boulevard
- Vista del Sol Drive
- Darrington Road
- Pellicano Drive
- Mission Ridge Boulevard Phase II

VRF II

- Eastlake Phase I



Projects in Design

– Darrington Road

- Widen to a 4 lane divided roadway from Eastlake to Pellicano
- PS&E Contract amount \$854,210.60
- **Invoiced to Date \$879,518.44**
- Amendment 1 \$91,860.52
Drainage Design and Survey
- **95% PS&E Submittal**
- Construction Estimate – \$9.9M
- Anticipated Letting – 2018



Projects in Design – Pellicano Drive



2013 EL PASO COUNTY COMPREHENSIVE MOBILITY PLAN

PROJECTS

VRF I

- Old Hueco Tanks Road
- Eastlake Phase II
- Rojas Drive
- Greg/Edgemere Extension
- Mission Ridge Boulevard
- Vista del Sol Drive
- Darrington Road
- Pellicano Drive
- Mission Ridge Boulevard Phase II

VRF II

- Eastlake Phase I



Projects in Design

– Pellicano Drive




- 6 lane divided roadway with 5' bike lanes, hike and bike trail, illumination, and landscaping
- Schematic, Environmental and PS&E
- CEA Engineering
- **Design Contract amount** **\$1,965,422.17**
- **Invoiced to Date** **\$304,583.23**
- August 2018 – Construction Letting (est.)
- Probable Cost \$17M (VRF 1 and Federal funding)

Projects in Design

– Pellicano Drive

CROSS SECTIONAL ELEMENTS

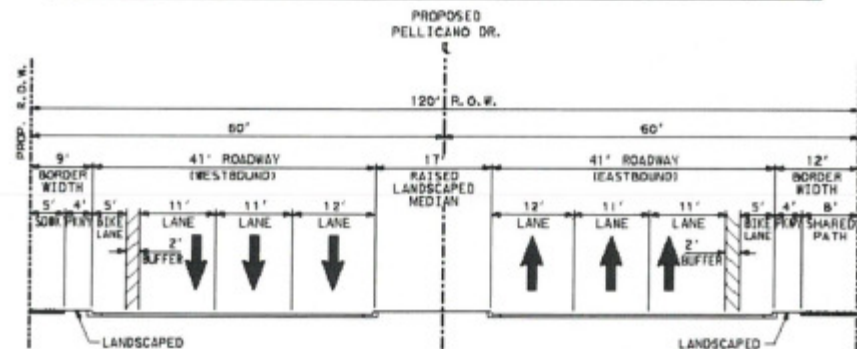

PROPOSED PELLICANO DR.
TYPICAL SECTION
(OPTION 3)




Projects in Construction

– Camino Real National Historic Trail



- Historic signage from San Elizario to Anthony, Texas
- 126 signs
- Contractor – Lesna Construction Inc.
- Bid amount – \$157,685.00
- **Final signs approved**
- **Mid-February – Signs will arrive**
- Contractor to start at Anthony/SL
- Contract time 3 months (est.)

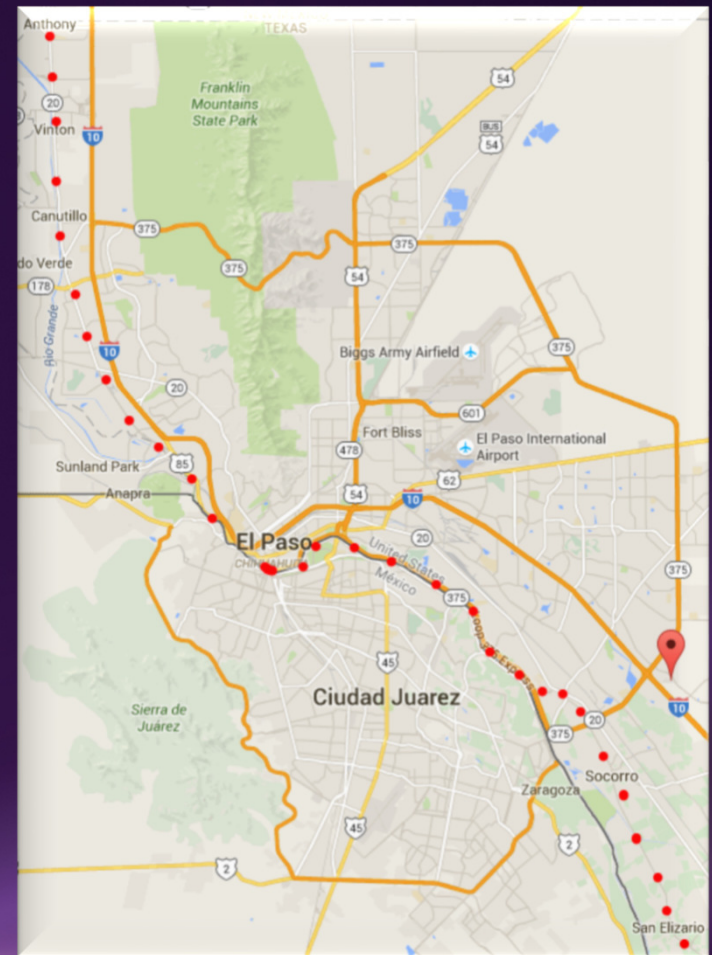

Projects in Construction

– Camino Real National Historic Trail



- Mock-up sign has been approved

Projects in Construction

– Vista Del Sol Dr.



2013 EL PASO COUNTY COMPREHENSIVE MOBILITY PLAN

PROJECTS

VRF I

- Old Hueco Tanks Road
- Eastlake Phase II
- Rojas Drive
- Greg/Edgemere Extension
- Mission Ridge Boulevard
- Vista del Sol Drive
- Darrington Road
- Pellicano Drive
- Mission Ridge Boulevard Phase II

VRF II

- Eastlake Phase I



Projects in Construction

– Vista Del Sol Dr.



- Widen to a 4 lane divided roadway from Loop 375 to Cherrington Dr.
- Bain Construction
- Contract Amount **\$4,582,190.00**
- **Invoiced to Date** **\$368,698.92**
- **Complete to Date** **8%**
- Start date October 11
- Working on the installation of storm sewer and EPWU sanitary sewer.

Projects in Construction

– Vista Del Sol Dr.

Phase I Sanitary Sewer Installation - From Addison St. to Cherrington Rd.



Projects in Construction

– Vista Del Sol Dr.

Phase I Storm Sewer Installation - From Addison St. to Cherrington St.



Projects in Construction

– Vista Del Sol Dr.

Phase I – New temporary detour road on Windermere Ave.



Projects in Construction

– Old Hueco Tanks Road



2013 EL PASO COUNTY COMPREHENSIVE MOBILITY PLAN

PROJECTS

VRF I

- Old Hueco Tanks Road
- Eastlake Phase II
- Rojas Drive
- Greg/Edgemere Extension
- Mission Ridge Boulevard
- Vista del Sol Drive
- Darrington Road
- Pellicano Drive
- Mission Ridge Boulevard Phase II

VRF II

- Eastlake Phase I



Projects in Construction

– Old Hueco Tanks Road



- New 4 lane divided roadway – **to be signed as *Nuevo Hueco Tanks Road***
- International Eagle Enterprises, Inc.
- Contract Amount **\$7,520,127.90**
- **Invoiced to Date** **\$7,198,381.77**
- **Complete to Date** **92%**
- Working on medians, drainage ponds, inlets and punch list items

Projects in Construction

– Old Hueco Tanks Road

Gateway East and Nuevo Hueco Tanks Rd



Projects in Construction

– Old Hueco Tanks Road



Projects in Construction

– Old Hueco Tanks Road



Projects in Construction

– Eastlake Phase 2



2013 EL PASO COUNTY COMPREHENSIVE MOBILITY PLAN

PROJECTS

VRF I

- Old Hueco Tanks Road
- Eastlake Phase II
- Rojas Drive
- Greg/Edgemere Extension
- Mission Ridge Boulevard
- Vista del Sol Drive
- Darrington Road
- Pellicano Drive
- Mission Ridge Boulevard Phase II

VRF II

- Eastlake Phase I



Projects in Construction

– Eastlake Phase 2



- Widen to a 6 lane divided roadway (Darrington Rd. to Horizon Blvd.)
- Jordan Foster Construction
- Contract Amount **\$13,464,149.00**
- Invoiced to Date **\$11,492,112.55**
- Complete to Date **85%**
- Working on embankment, excavation, base, HMAC, storm sewer, inlets.

Projects in Construction

– Eastlake Phase 2

Phase I & II Finished – From Darrington Rd. to Horizon Mesa Dr.



Projects in Construction

– Eastlake Phase 2

Phase III TCP – From Horizon Mesa to Desert Mist Dr.



Projects in Construction

– Eastlake Phase 2

Phase IV Under Construction – From Horizon Mesa to Desert Mist Dr.



Projects in Construction

– Eastlake Phase 2

Phase V – From Desert Mist Dr. to Horizon Blvd.



Projects in Construction

– Eastlake Phase 2



Phase VI – Eastlake Blvd. and Horizon Blvd. Intersection



Projects in Construction

– Rojas Drive



2013 EL PASO COUNTY COMPREHENSIVE MOBILITY PLAN

PROJECTS

VRF I

-  Old Hueco Tanks Road
-  Eastlake Phase II
-  Rojas Drive
-  Greg/Edgemere Extension
-  Mission Ridge Boulevard
-  Vista del Sol Drive
-  Darrington Road
-  Pellicano Drive
-  Mission Ridge Boulevard Phase II

VRF II

-  Eastlake Phase I



Projects in Construction

– Rojas Drive



- Widen Rojas to a 6 lane divided roadway (El Paso City limits to Eastlake Blvd.)
- Horizone Construction, LTD
- Contract **\$3,843,033.70**
- Invoiced to Date **\$1,325,536.99**
- Complete to Date **34%**
- Working on Phase 1B & 2B, concrete paving
- Various utility conflicts have been resolved

Projects in Construction

– Rojas Drive



Rojas at Eastlake



Projects in Construction

– Rojas Drive



Spectrum Cable relocation complete



Projects in Construction – Rojas Drive



Chapel Hill Rd.



Projects in Construction

– Rojas Drive



Equestrian Rd.



Projects in Construction

– Rojas Drive



Water line conflicts resolved near Bill Burnett



Projects in Construction

– Eastlake Phase I



2013 EL PASO COUNTY COMPREHENSIVE MOBILITY PLAN

PROJECTS

VRF I

- Old Hueco Tanks Road
- Eastlake Phase II
- Rojas Drive
- Greg/Edgemere Extension
- Mission Ridge Boulevard
- Vista del Sol Drive
- Darrington Road
- Pellicano Drive
- Mission Ridge Boulevard Phase II

VRF II

- Eastlake Phase I



Projects in Construction

– Eastlake Phase I



- Widen to 6 lane divided roadway with raised median (I-10 to Darrington Rd.)
- **Project Let January 11, 2018**
- **Construction Schedule (approx.) 18 Months**
- **Possible start in April 2018**
- 1st Phase, Stages A, B, and C, Construct the NB Side Rojas To Darrington

Projects in Construction

– Greg/Edgemere Extension



2013 EL PASO COUNTY COMPREHENSIVE MOBILITY PLAN

PROJECTS

VRF I

- Old Hueco Tanks Road
- Eastlake Phase II
- Rojas Drive
- Greg/Edgemere Extension
- Mission Ridge Boulevard
- Vista del Sol Drive
- Darrington Road
- Pellicano Drive
- Mission Ridge Boulevard Phase II

VRF II

- Eastlake Phase I



Projects Funded by CRRMA

– Greg/Edgemere Extension Project



- **Greg/Edgemere Extension – 4 lanes divided w/ bike lanes (Edgemere Blvd east 1.3 miles to Greg Rd.)**
- **CRRMA funding the construction via payment to County – \$2.5M**
- **Work done thru a County Developer Participation Agreement**
- **Dirt Work and C&G**

Projects Funded by CRRMA

– Greg/Edgemere Extension Project



Edgemere Blvd @ Nevil Shed St.



Projects Funded by CRRMA

– Greg/Edgemere Extension Project



Edgemere Blvd



Projects Funded by CRRMA

– Greg/Edgemere Extension Project



Water and sanitary sewer work near Vista Del Este



Projects Funded by CRRMA

– Greg/Edgemere Extension Project



Greg Rd.



Questions?



Camino Real Regional Mobility Authority

801 Texas Avenue

El Paso, Texas 79901

(915) 212-1072

info@crrma.org

www.crrma.org

