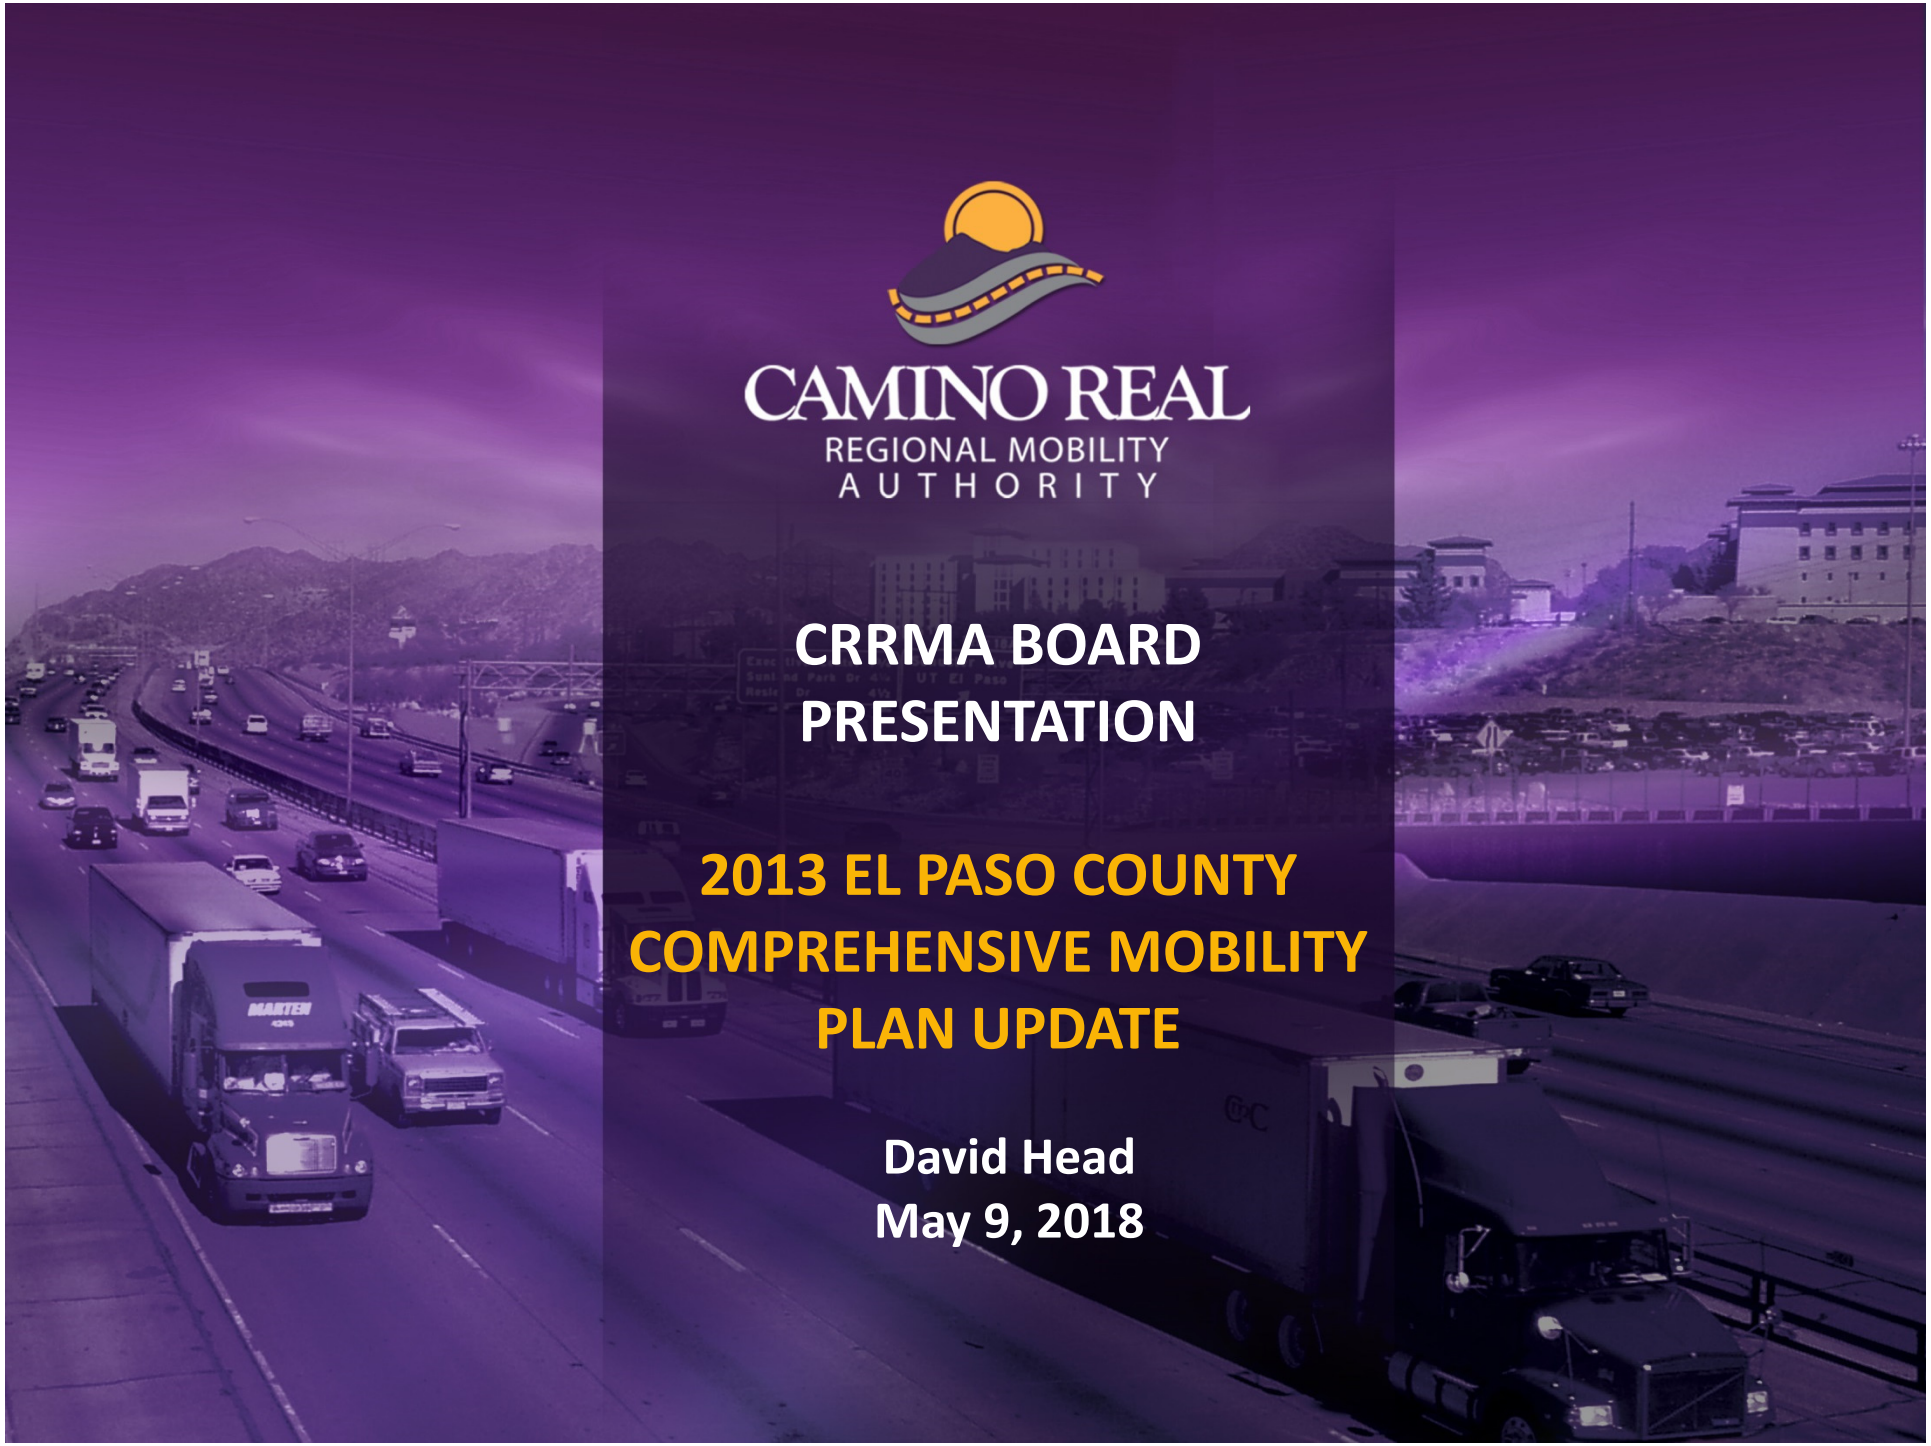

CAMINO REAL
REGIONAL MOBILITY
AUTHORITY

CRRMA BOARD PRESENTATION

2013 EL PASO COUNTY COMPREHENSIVE MOBILITY PLAN UPDATE

David Head
May 9, 2018

2013 El Paso County Comprehensive Mobility Plan

CAMINO REAL REGIONAL MOBILITY AUTHORITY

AGENDA

- 2013 CMP Project Map
- Project Listing
- Project Updates
  - Projects in Design
  - Projects under Construction
  - Projects being Funded by CRRMA

2013 CMP Project Map

CAMINO REAL REGIONAL MOBILITY AUTHORITY

CAMINO REAL REGIONAL MOBILITY AUTHORITY

2013 EL PASO COUNTY COMPREHENSIVE MOBILITY PLAN

PROJECTS

VRF I

- Old Hueco Tanks Road
- Eastlake Phase II
- Rojas Drive
- Greg/Edgemere Extension
- Mission Ridge Boulevard
- Vista del Sol Drive
- Darrington Road
- Pellicano Drive
- Mission Ridge Boulevard Phase II

VRF II

- Eastlake Phase I

EL PASO COUNTY

2013 CMP County/CRRMA Projects

CAMINO REAL REGIONAL MOBILITY AUTHORITY

Projects in Design:

- Darrington Rd. (From Eastlake to Pellicano)
- Mission Ridge II (From Mission Ridge I to ½ mile south)
- Pellicano (From Lp375 to Darrington Rd.)

Projects under Construction:

- El Camino Real de Tierra Adentro National Historic Trail (Along SH 20 from Chicken Rd. to NM/TX state line)
- Vista Del Sol Dr. (From Loop 375 to Cherrington Dr.)
- Old Hueco Tanks (From North Loop to I-10)
- Eastlake 2 (From Darrington Rd. to Horizon Blvd)
- Rojas Dr. (From Bill Burnett Dr. to Eastlake Blvd.)
- Eastlake I (From I-10 to Darrington Rd.)

Projects being Funded by the CRRMA:

- Greg/Edgemere (From Edgemere Blvd. east to Greg Rd.)

Projects in Design – Darrington Road

CAMINO REAL REGIONAL MOBILITY AUTHORITY

CAMINO REAL REGIONAL MOBILITY AUTHORITY

2013 EL PASO COUNTY COMPREHENSIVE MOBILITY PLAN

PROJECTS

VRF I

- Old Hueco Tanks Road
- Eastlake Phase II
- Rojas Drive
- Greg/Edgemere Extension
- Mission Ridge Boulevard
- Vista del Sol Drive
- Darrington Road
- Pellicano Drive
- Mission Ridge Boulevard Phase II

VRF II

- Eastlake Phase I

Projects in Design – Darrington Road

CAMINO REAL REGIONAL MOBILITY AUTHORITY

- Widen to a 4 lane divided roadway from Eastlake to Pellicano
- PS&E Contract amount $946071.16
- Invoiced to Date $895,615.50
- Amendment 2 (Pending) Pellicano Intersection and drainage redesign
- 95% PS&E Submittal
- Construction Estimate – $9.9M
- Anticipated Letting – 2018

Projects in Design – Pellicano Drive

CAMINO REAL REGIONAL MOBILITY AUTHORITY

CAMINO REAL REGIONAL MOBILITY AUTHORITY

2013 EL PASO COUNTY COMPREHENSIVE MOBILITY PLAN

PROJECTS

VRF I

- Old Hueco Tanks Road
- Eastlake Phase II
- Rojas Drive
- Greg/Edgemere Extension
- Mission Ridge Boulevard
- Vista del Sol Drive
- Darrington Road
- Pellicano Drive
- Mission Ridge Boulevard Phase II

VRF II

- Eastlake Phase I

EL PASO COUNTY

Projects in Design – Pellicano Drive

CAMINO REAL REGIONAL MOBILITY AUTHORITY

- 6 lane divided roadway with 5’ bike lanes, hike and bike trail, illumination, and landscaping
- PS&E Contract amount $1,965,422.17
- Invoiced to Date $667,176.38
- 60% Schematic/30% Design
- Spring 2019 – Construction Letting (est.)
- Probable Cost $17M (VRF 1 and Federal funding)

Projects in Construction – Camino Real National Historic Trail

CAMINO REAL REGIONAL MOBILITY AUTHORITY

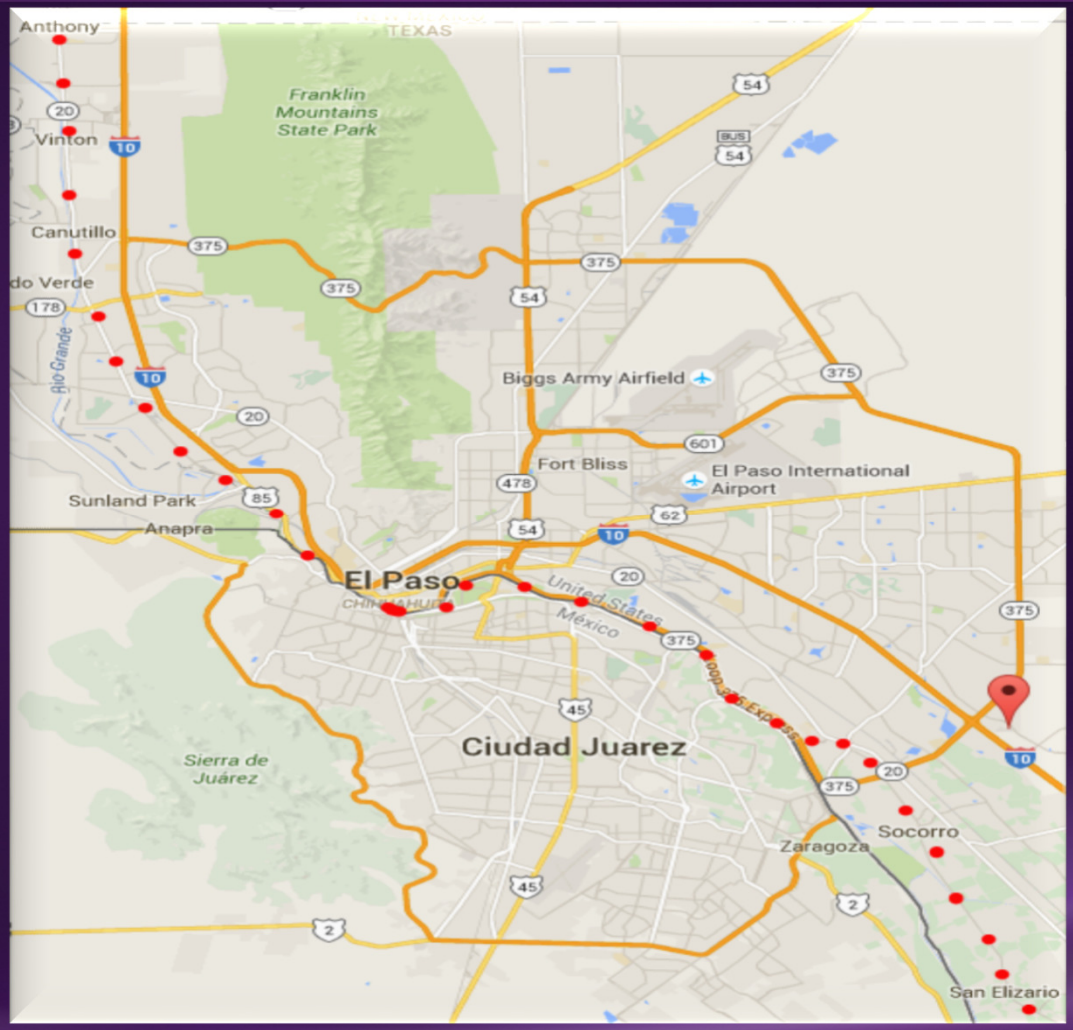

Projects in Construction – Camino Real National Historic Trail

CAMINO REAL REGIONAL MOBILITY AUTHORITY

- Historic signage from San Elizario to Anthony, Texas
- 121 signs
- Contractor – Lesna Construction Inc.
- Bid amount – $157,685.00
- Invoiced to Date $46,500 MOH
- Started placing foundations and signs
- Contractor started at Anthony/SL
- Contract time 3 months (est.)

Projects in Construction – Camino Real National Historic Trail

CAMINO REAL REGIONAL MOBILITY AUTHORITY

First sign installed on 4-24-18 Antonio St. and E Frontage Rd.

55 Sign foundations installed

Projects in Construction – Vista Del Sol Dr.

CAMINO REAL REGIONAL MOBILITY AUTHORITY

CAMINO REAL REGIONAL MOBILITY AUTHORITY

2013 EL PASO COUNTY COMPREHENSIVE MOBILITY PLAN

PROJECTS

VRF I

- Old Hueco Tanks Road
- Eastlake Phase II
- Rojas Drive
- Greg/Edgemere Extension
- Mission Ridge Boulevard
- Vista del Sol Drive
- Darrington Road
- Pellicano Drive
- Mission Ridge Boulevard Phase II

VRF II

- Eastlake Phase I

EL PASO COUNTY

Projects in Construction – Vista Del Sol Dr.

CAMINO REAL REGIONAL MOBILITY AUTHORITY

- Widen to a 4 lane divided roadway from Loop 375 to Cherrington Dr.
- Bain Construction
- Contract Amount $4,582,190.00
- Invoiced to Date $746,448.00
- Complete to Date 16%
- Working on the installation of storm sewer and EPWU water main.

Projects in Construction – Vista Del Sol Dr.

CAMINO REAL REGIONAL MOBILITY AUTHORITY

Phase I Sanitary Sewer Installation Completed

Projects in Construction – Vista Del Sol Dr.

CAMINO REAL REGIONAL MOBILITY AUTHORITY

Phase I Water Main Installation

Projects in Construction – Vista Del Sol Dr.

CAMINO REAL REGIONAL MOBILITY AUTHORITY

Phase I – New temporary detour road from Paseo del Norte to Addison St.

Projects in Construction – Old Hueco Tanks Road

CAMINO REAL REGIONAL MOBILITY AUTHORITY

CAMINO REAL REGIONAL MOBILITY AUTHORITY

2013 EL PASO COUNTY COMPREHENSIVE MOBILITY PLAN

PROJECTS

VRF I

- Old Hueco Tanks Road
- Eastlake Phase II
- Rojas Drive
- Greg/Edgemere Extension
- Mission Ridge Boulevard
- Vista del Sol Drive
- Darrington Road
- Pellicano Drive
- Mission Ridge Boulevard Phase II

VRF II

- Eastlake Phase I

Projects in Construction – Old Hueco Tanks Road

CAMINO REAL REGIONAL MOBILITY AUTHORITY

- New 4 lane divided roadway – to be signed as *Nuevo Hueco Tanks Road*
- International Eagle Enterprises, Inc.
- Contract Amount $7,815,488.28
- Invoiced to Date $7,459,592.13
- Complete to Date 95%
- Working on clean up and punch list items and TxDOT federal oversight reviews

Projects in Construction – Old Hueco Tanks Road

CAMINO REAL REGIONAL MOBILITY AUTHORITY

New Signs

Projects in Construction – Old Hueco Tanks Road

CAMINO REAL REGIONAL MOBILITY AUTHORITY

Looking South

Projects in Construction – Old Hueco Tanks Road

CAMINO REAL REGIONAL MOBILITY AUTHORITY

Nuevo Hueco Tanks at North Loop

Projects in Construction – Eastlake Phase 2

CAMINO REAL REGIONAL MOBILITY AUTHORITY

CAMINO REAL REGIONAL MOBILITY AUTHORITY

2013 EL PASO COUNTY COMPREHENSIVE MOBILITY PLAN

PROJECTS

VRF I

- Old Hueco Tanks Road
- Eastlake Phase II
- Rojas Drive
- Greg/Edgemere Extension
- Mission Ridge Boulevard
- Vista del Sol Drive
- Darrington Road
- Pellicano Drive
- Mission Ridge Boulevard Phase II

VRF II

- Eastlake Phase I

EL PASO COUNTY

Projects in Construction – Eastlake Phase 2

CAMINO REAL REGIONAL MOBILITY AUTHORITY

- Widen to a 6 lane divided roadway (Darrington Rd. to Horizon Blvd.)
- Jordan Foster Construction
- Contract Amount $13,709,239.00
- Invoiced to Date $13,342,380.00
- Complete to Date 97%
- Working on punch list items and pending approvals for testing and TDLR formal acceptance.

Projects in Construction – Eastlake Phase 2

CAMINO REAL REGIONAL MOBILITY AUTHORITY

Ribbon Cutting Ceremony 4-11-18

Projects in Construction – Eastlake Phase 2

CAMINO REAL REGIONAL MOBILITY AUTHORITY

First vehicles driving on the new Eastlake Blvd.

Projects in Construction – Eastlake Phase 2

CAMINO REAL REGIONAL MOBILITY AUTHORITY

New Eastlake Blvd. and Horizon Blvd. Intersection

Projects in Construction – Eastlake Phase 2

CAMINO REAL REGIONAL MOBILITY AUTHORITY

New Eastlake Blvd. and Kenazo Ave. Intersection

Projects in Construction – Rojas Drive

CAMINO REAL REGIONAL MOBILITY AUTHORITY

CAMINO REAL REGIONAL MOBILITY AUTHORITY

2013 EL PASO COUNTY COMPREHENSIVE MOBILITY PLAN

PROJECTS

VRF I

- Old Hueco Tanks Road
- Eastlake Phase II
- Rojas Drive
- Greg/Edgemere Extension
- Mission Ridge Boulevard
- Vista del Sol Drive
- Darrington Road
- Pellicano Drive
- Mission Ridge Boulevard Phase II

VRF II

- Eastlake Phase I

EL PASO COUNTY

Projects in Construction – Rojas Drive

CAMINO REAL REGIONAL MOBILITY AUTHORITY

- Widen Rojas to a 6 lane divided roadway (El Paso City limits to Eastlake Blvd.)
- Horizone Construction, LTD
- Contract $3,843,033.70
- Invoiced to Date $1,764,557.55
- Complete to Date 45%
- Working on Phase 2A, storm sewer, concrete paving
- Various utility conflicts have been resolved

Projects in Construction – Rojas Drive

CAMINO REAL REGIONAL MOBILITY AUTHORITY

Paving along Rojas phase 2A

Projects in Construction – Rojas Drive

CAMINO REAL REGIONAL MOBILITY AUTHORITY

Storm Sewer Work

Projects in Construction – Rojas Drive

CAMINO REAL REGIONAL MOBILITY AUTHORITY

Rojas at Bill Burnet

Projects in Construction – Eastlake Phase I

CAMINO REAL REGIONAL MOBILITY AUTHORITY

CAMINO REAL REGIONAL MOBILITY AUTHORITY

2013 EL PASO COUNTY COMPREHENSIVE MOBILITY PLAN

PROJECTS

VRF I

- Old Hueco Tanks Road
- Eastlake Phase II
- Rojas Drive
- Greg/Edgemere Extension
- Mission Ridge Boulevard
- Vista del Sol Drive
- Darrington Road
- Pellicano Drive
- Mission Ridge Boulevard Phase II

VRF II

- Eastlake Phase I

EL PASO COUNTY

Projects in Construction – Eastlake Phase I

CAMINO REAL REGIONAL MOBILITY AUTHORITY

- Widen to 6 lane divided roadway with raised median (I-10 to Darrington Rd.)
- Project Let January 11, 2018
- Construction Schedule (approx.) 18 Months
- Preconstruction meeting held April 17, 2018
- Construction started Monday, May 7, 2018
- 1st Phase, Stages A, B, and C, Construct the NB Side Rojas To Darrington

Projects in Construction – Greg/Edgemere Extension

CAMINO REAL REGIONAL MOBILITY AUTHORITY

CAMINO REAL REGIONAL MOBILITY AUTHORITY

2013 EL PASO COUNTY COMPREHENSIVE MOBILITY PLAN

PROJECTS

VRF I

- Old Hueco Tanks Road
- Eastlake Phase II
- Rojas Drive
- Greg/Edgemere Extension
- Mission Ridge Boulevard
- Vista del Sol Drive
- Darrington Road
- Pellicano Drive
- Mission Ridge Boulevard Phase II

VRF II

- Eastlake Phase I

Projects Funded by CRRMA – Greg/Edgemere Extension Project

CAMINO REAL REGIONAL MOBILITY AUTHORITY

- Greg/Edgemere Extension – 4 lanes divided w/ bike lanes (Edgemere Blvd east 1.3 miles to Greg Rd.)
- CRRMA funding the construction via payment to County – $2.5M
- Work done thru a County Developer Participation Agreement
- Subgrade, base and paving

Projects Funded by CRRMA – Greg/Edgemere Extension Project

CAMINO REAL REGIONAL MOBILITY AUTHORITY

Edgemere Blvd

Projects Funded by CRRMA – Greg/Edgemere Extension Project

CAMINO REAL REGIONAL MOBILITY AUTHORITY

New Turnaround @ Edgemere and Vista Del Este

Projects Funded by CRRMA – Greg/Edgemere Extension Project

CAMINO REAL REGIONAL MOBILITY AUTHORITY

Greg Rd

Questions?

CAMINO REAL
REGIONAL MOBILITY
AUTHORITY

Camino Real Regional Mobility Authority
801 Texas Avenue
El Paso, Texas 79901
(915) 212-1072
info@crrma.org
www.crrma.org
