CAMINO REAL
REGIONAL MOBILITY
AUTHORITY

CRRMA BOARD PRESENTATION

2013 EL PASO COUNTY COMPREHENSIVE MOBILITY PLAN UPDATE

Raymond Telles

June 8, 2022

2013 El Paso County Comprehensive Mobility Plan

CAMINO REAL REGIONAL MOBILITY AUTHORITY

AGENDA

- 2013 CMP Project Map
- Project Listing
- Project Updates
  - Projects in Design
  - Projects under Construction
  - Projects Constructed

2013 CMP Project Map

CAMINO REAL REGIONAL MOBILITY AUTHORITY

CAMINO REAL REGIONAL MOBILITY AUTHORITY

2013 EL PASO COUNTY COMPREHENSIVE MOBILITY PLAN

PROJECTS

VRF I

- Old Hueco Tanks Road
- Eastlake Phase II
- Rojas Drive
- Greg/Edgemere Extension
- Mission Ridge Boulevard
- Vista del Sol Drive
- Darrington Road
- Pellicano Drive
- Mission Ridge Boulevard Phase II

VRF II

- Eastlake Phase I

2013 CMP Project List

CAMINO REAL REGIONAL MOBILITY AUTHORITY

Projects in Design:

- Darrington Rd. (From Eastlake to Pellicano)

Projects under Construction:

- Pellicano (From LP-375 to Darrington Rd.)
- Mission Ridge II (From Mission Ridge I to ½ mile south)
- Eastlake I (From I-10 to Darrington Rd.)

Completed Projects:

- Greg/Edgemere (From Edgemere Blvd. east to Greg Rd.)
- Old Hueco Tanks (From North Loop to I-10)
- El Camino Real de Tierra Adentro National Historic Trail (Along SH 20 from Chicken Rd. to NM/TX state line)
- Eastlake 2 (From Darrington Rd. to Horizon Blvd)
- Rojas Dr. (From Bill Burnett Dr. to Eastlake Blvd.)
- Vista Del Sol Dr. (From Loop 375 to Cherrington Dr.)

Projects in Design – Darrington Road

CAMINO REAL REGIONAL MOBILITY AUTHORITY

CAMINO REAL REGIONAL MOBILITY AUTHORITY

2013 EL PASO COUNTY COMPREHENSIVE MOBILITY PLAN

PROJECTS

VRF I

- Old Hueco Tanks Road
- Eastlake Phase II
- Rojas Drive
- Greg/Edgemere Extension
- Mission Ridge Boulevard
- Vista del Sol Drive
- Darrington Road
- Pellicano Drive
- Mission Ridge Boulevard Phase II

VRF II

- Eastlake Phase I

EL PASO COUNTY

Projects in Design – Darrington Road

CAMINO REAL REGIONAL MOBILITY AUTHORITY

- Widen to a 4 lane divided roadway from Eastlake to Pellicano
- PS&E Contract amount $1,063,474.28
- Invoiced to Date $1,046,473.09
- Preliminary concrete design
- Construction Estimate - $19M
- Anticipated Letting – Winter 2022

Projects in Construction – Pellicano Drive

CAMINO REAL REGIONAL MOBILITY AUTHORITY

CAMINO REAL REGIONAL MOBILITY AUTHORITY

2013 EL PASO COUNTY COMPREHENSIVE MOBILITY PLAN

PROJECTS

VRF I

- Old Hueco Tanks Road
- Eastlake Phase II
- Rojas Drive
- Greg/Edgemere Extension
- Mission Ridge Boulevard
- Vista del Sol Drive
- Darrington Road
- Pellicano Drive
- Mission Ridge Boulevard Phase II

VRF II

- Eastlake Phase I

EL PASO COUNTY

Projects in Construction – Pellicano Drive

CAMINO REAL REGIONAL MOBILITY AUTHORITY

- 6 lane divided roadway with bike lanes, hike and bike trail, illumination and landscaping
- JAR Concrete
- Contract Amount $21,655,645.80
- Contract Amount (w/COs) $21,921,475.85
- Invoiced to Date $ 9,457,292.03
- Complete to Date 43.14%
- Installation of concrete pavement, embankment, excavation of swales and installation of water loops

Projects in Construction – Pellicano Drive

CAMINO REAL REGIONAL MOBILITY AUTHORITY

Looking west – Installation of concrete pavement from Sun Fire Blvd. to Mission Ridge Blvd.

Projects in Construction – Pellicano Drive

CAMINO REAL REGIONAL MOBILITY AUTHORITY

Looking west – Embankment between Joe Battle Blvd. and Sun Fire Blvd.

Projects in Construction – Pellicano Drive

CAMINO REAL REGIONAL MOBILITY AUTHORITY

Looking east – Installation of concrete pavement by Joe Battle Blvd. And Pellicano Dr. intersection

Projects in Construction – Pellicano Drive

CAMINO REAL REGIONAL MOBILITY AUTHORITY

Looking west – Installation of water loops

Projects in Construction – Pellicano Drive

CAMINO REAL REGIONAL MOBILITY AUTHORITY

Looking east – Reshaping swales and installation of rock riprap

Projects in Construction – Mission Ridge Phase II

CAMINO REAL REGIONAL MOBILITY AUTHORITY

CAMINO REAL REGIONAL MOBILITY AUTHORITY

2013 EL PASO COUNTY COMPREHENSIVE MOBILITY PLAN

PROJECTS

VRF I

- Old Hueco Tanks Road
- Eastlake Phase II
- Rojas Drive
- Greg/Edgemere Extension
- Mission Ridge Boulevard
- Vista del Sol Drive
- Darrington Road
- Pellicano Drive
- Mission Ridge Boulevard Phase II

VRF II

- Eastlake Phase I

EL PASO COUNTY

Projects in Construction – Mission Ridge Phase II

CAMINO REAL REGIONAL MOBILITY AUTHORITY

- 6 lane divided roadway with raised median, asphalt pavement, curb and gutter, sidewalk, landscaping, illumination and storm drainage
- JAR Concrete
- Contract Amount $5,162,216.00
- Contract Amount (w/COs) $5,828,503.72
- Invoiced to Date $5,528,060.03
- Complete to Date 94. 85%
- Constructing rock wall
- Completed sanitary sewer line

Projects in Construction – Mission Ridge Blvd. Phase II

CAMINO REAL REGIONAL MOBILITY AUTHORITY

Hike & bike path in front of pond

Projects in Construction – Mission Ridge Blvd. Phase II

CAMINO REAL REGIONAL MOBILITY AUTHORITY

Embankment work around the pond

Projects in Construction – Mission Ridge Blvd. Phase II

CAMINO REAL REGIONAL MOBILITY AUTHORITY

Rock wall work around pond

Projects in Construction – Eastlake Phase I

CAMINO REAL REGIONAL MOBILITY AUTHORITY

CAMINO REAL REGIONAL MOBILITY AUTHORITY

2013 EL PASO COUNTY COMPREHENSIVE MOBILITY PLAN

PROJECTS

VRF I

- Old Hueco Tanks Road
- Eastlake Phase II
- Rojas Drive
- Greg/Edgemere Extension
- Mission Ridge Boulevard
- Vista del Sol Drive
- Darrington Road
- Pellicano Drive
- Mission Ridge Boulevard Phase II

VRF II

- Eastlake Phase I

EL PASO COUNTY

Projects in Construction – Eastlake Phase I

CAMINO REAL REGIONAL MOBILITY AUTHORITY

- Widen to 6 lane divided roadway with raised median (I-10 to Darrington Rd.)
- JD Abrams, LLP
- Contract Amount $23,653,752.53
- Contract Amount (w/COs) $ 25,786,632.50
- Invoiced to Date $25,786,632.50
- Complete to Date 100.00%
- Roadway open to traffic
- Eastlake Boulevard project has been completed.

Projects in Construction – Eastlake Phase I

CAMINO REAL REGIONAL MOBILITY AUTHORITY

Stem wall work- Looking north from Rojas Dr.

Projects in Construction – Eastlake Phase I

CAMINO REAL REGIONAL MOBILITY AUTHORITY

Cleanup Phase - Looking north from Emerald Park Dr.

Completed Projects – Vista Del Sol Dr.

CAMINO REAL REGIONAL MOBILITY AUTHORITY

CAMINO REAL REGIONAL MOBILITY AUTHORITY

2013 EL PASO COUNTY COMPREHENSIVE MOBILITY PLAN

PROJECTS

VRF I

- Old Hueco Tanks Road
- Eastlake Phase II
- Rojas Drive
- Greg/Edgemere Extension
- Mission Ridge Boulevard
- Vista del Sol Drive
- Darrington Road
- Pellicano Drive
- Mission Ridge Boulevard Phase II

VRF II

- Eastlake Phase I

EL PASO COUNTY

Completed Projects – Vista Del Sol Dr.

CAMINO REAL REGIONAL MOBILITY AUTHORITY

- Widen to a 4 lane divided roadway from LP375 to Cherrington Dr.
- Bain Construction
- Contract Amount $4,582,190.00
- Contract Amount (w/COs) $4,989,486.70
- Invoiced to Date $4,989,486.70
- Complete to Date 100%
- Open to traffic
- Project is complete

Completed Projects – Greg/Edgemere Extension

CAMINO REAL REGIONAL MOBILITY AUTHORITY

CAMINO REAL REGIONAL MOBILITY AUTHORITY

2013 EL PASO COUNTY COMPREHENSIVE MOBILITY PLAN

PROJECTS

VRF I

- Old Hueco Tanks Road
- Eastlake Phase II
- Rojas Drive
- Greg/Edgemere Extension
- Mission Ridge Boulevard
- Vista del Sol Drive
- Darrington Road
- Pellicano Drive
- Mission Ridge Boulevard Phase II

VRF II

- Eastlake Phase I

Completed Projects – Greg/Edgemere Extension Project

CAMINO REAL REGIONAL MOBILITY AUTHORITY

- Greg/Edgemere Extension – 4 lanes divided w/ bike lanes (Edgemere Blvd east 1.3 miles to Greg Rd.)
- CRRMA funding the construction via payment to County – $ 2,475,819.14
- Work done thru a County Developer Participation Agreement
- Open to traffic
- Project is complete

Completed Projects – Old Hueco Tanks Road

CAMINO REAL REGIONAL MOBILITY AUTHORITY

CAMINO REAL REGIONAL MOBILITY AUTHORITY

2013 EL PASO COUNTY COMPREHENSIVE MOBILITY PLAN

PROJECTS

VRF I

- Old Hueco Tanks Road
- Eastlake Phase II
- Rojas Drive
- Greg/Edgemere Extension
- Mission Ridge Boulevard
- Vista del Sol Drive
- Darrington Road
- Pellicano Drive
- Mission Ridge Boulevard Phase II

VRF II

- Eastlake Phase I

Completed Projects – Old Hueco Tanks Road

CAMINO REAL REGIONAL MOBILITY AUTHORITY

- New 4 lane divided roadway – Signed as *Nuevo Hueco Tanks Road*
- International Eagle Enterprises, Inc.
- Contract Amount $7,520,127.90
- Contract Amount (w/COs) $7,601,890.60
- Invoiced to Date $7,601,890.60
- Complete to Date 100.00%
- Open to traffic
- Project is completed

Completed Projects – Camino Real National Historic Trail

CAMINO REAL REGIONAL MOBILITY AUTHORITY

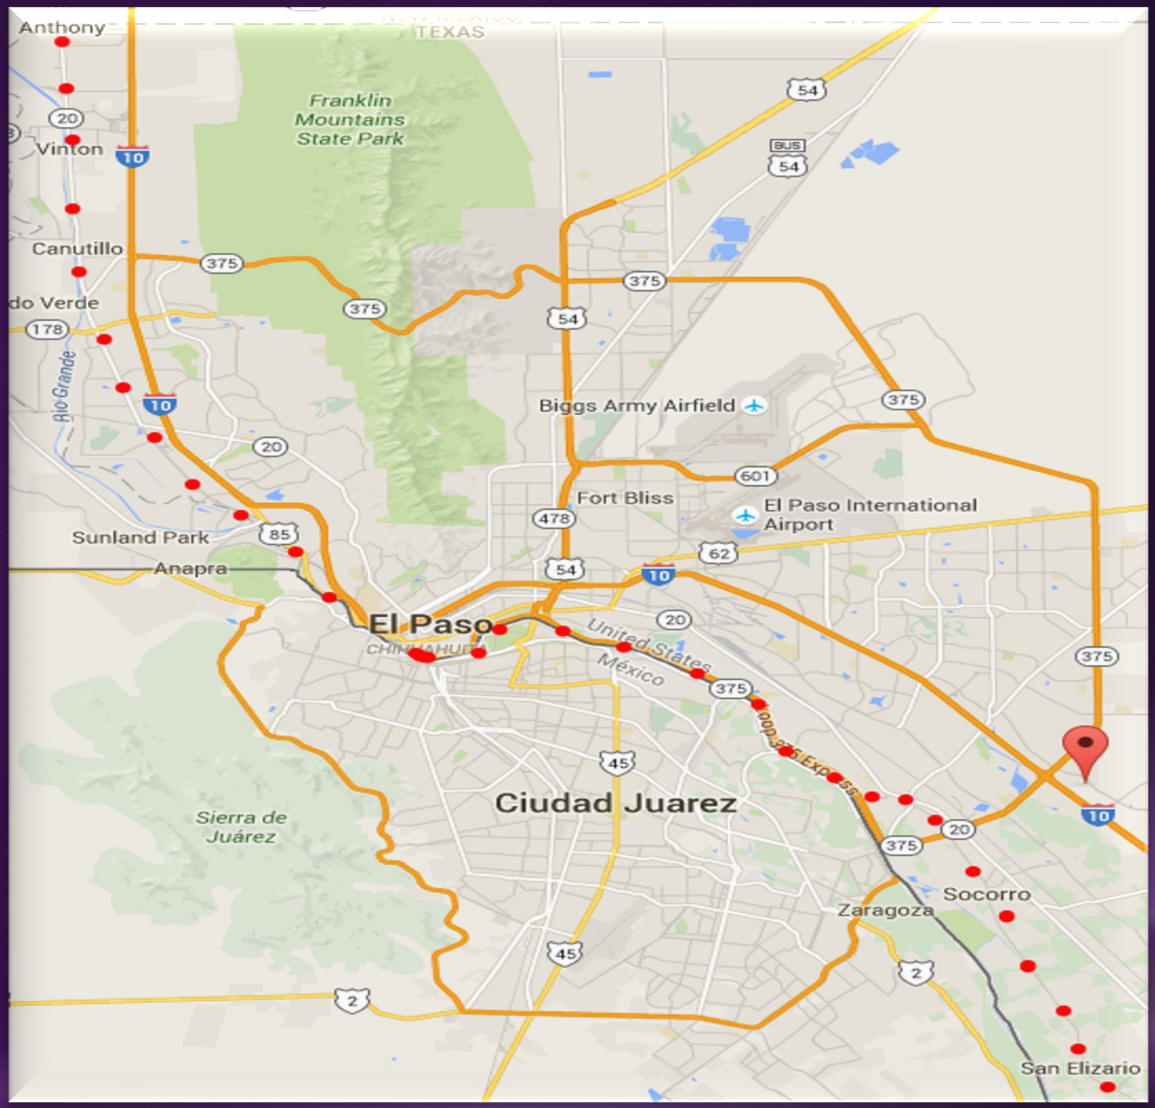

Completed Projects – Camino Real National Historic Trail

CAMINO REAL REGIONAL MOBILITY AUTHORITY

- Historic signage from San Elizario to Anthony, Texas
- Lesna Construction Inc.
- Contract Amount $157,685.00
- Adjusted Contract Amount With Change Orders $157,187.88
- Invoiced to Date $157,187.88
- Complete to date 100%
- Project is complete

Completed Projects – Eastlake Phase 2

CAMINO REAL REGIONAL MOBILITY AUTHORITY

CAMINO REAL REGIONAL MOBILITY AUTHORITY

2013 EL PASO COUNTY COMPREHENSIVE MOBILITY PLAN

PROJECTS

VRF I

- Old Hueco Tanks Road
- Eastlake Phase II
- Rojas Drive
- Greg/Edgemere Extension
- Mission Ridge Boulevard
- Vista del Sol Drive
- Darrington Road
- Pellicano Drive
- Mission Ridge Boulevard Phase II

VRF II

- Eastlake Phase I

Completed Projects – Eastlake Phase 2

CAMINO REAL REGIONAL MOBILITY AUTHORITY

- Widen to a 6 lane divided roadway (Darrington Rd. to Horizon Blvd.)
- Jordan Foster Construction
- Contract Amount $13,464,149.00
- Adjusted Contract Amount With Change Orders $13,772,538.58
- Invoiced to Date $13,772,538.58
- Complete to Date 100%
- Project is complete

Completed Projects – Rojas Drive

CAMINO REAL REGIONAL MOBILITY AUTHORITY

CAMINO REAL REGIONAL MOBILITY AUTHORITY

2013 EL PASO COUNTY COMPREHENSIVE MOBILITY PLAN

PROJECTS

VRF I

- Old Hueco Tanks Road
- Eastlake Phase II
- Rojas Drive
- Greg/Edgemere Extension
- Mission Ridge Boulevard
- Vista del Sol Drive
- Darrington Road
- Pellicano Drive
- Mission Ridge Boulevard Phase II

VRF II

- Eastlake Phase I

Completed Projects – Rojas Drive

CAMINO REAL REGIONAL MOBILITY AUTHORITY

- Widen Rojas to a 6 lane divided roadway (El Paso City limits to Eastlake Blvd.)
- Horizone Construction, LTD
- Contract Amount $3,843,033.70
- Contract Amount (w/COs) $3,905,601.55
- Invoiced to Date $3,905,601.55
- Complete to Date 100%
- Project is complete

Questions?

CAMINO REAL
REGIONAL MOBILITY
AUTHORITY

Camino Real Regional Mobility Authority
801 Texas Avenue
El Paso, Texas 79901
(915) 212-1072
info@crrma.org
www.crrma.org
